

Masslak Implementation Timeline

Interfaces, programming, databases and system preparation from Phase 0 to launch, based on sections 20 to 22 of the Analysis and Design Study v2.5. Work starts on Monday 5 October 2026.


End of Phase 0 November 2026 Friday 27	Pilot launch October 2027 Monday 4	Phase 1 closed November 2027 Friday 26	Shuttle go-live April 2028 Friday 7
---	---	---	--

Planned task Already built in the repository Milestone Ramadan and Eid (approximate) Today

Phases	Phase 0		Sprint a: core		Sprint b: fleet		Sprint c: booking and money		Sprint d: operations		Sprint e: hardening		Pilot		Phase 2: shuttle				
Months	Oct 2026	Nov	Dec	Jan 2027	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec	Jan 2028	Feb	Mar	Apr
Milestones	Today																		
Phase 0 gate passed22.1																			
Company registration and approval22.2 a																			
Trips published22.2 b																			
Full booking and payment22.2 c																			
Operational readiness22.2 d																			
Pilot launch22.3																			
Phase 1 closed2.7																			
Shuttle go-live21																			
Interfaces																			
Visual identity and design system3.6																			
UX research and portal prototype24																			
Arabic and English interface shell3.5																			
Sign-up, sign-in and carrier approval screens32																			
Fleet, station, route and trip pattern screens32																			
Search, seat map, checkout, wallet and tickets32																			
Agency portal and admin back office3.5																			
Android and iOS apps for passengers and operators3.5																			
Driver app: QR scan, manifest and location lock7.13																			
Regulator dashboard and report screens35																			
Usability and accessibility testing36																			
Shuttle screens: subscriptions, vehicle sticker, segment fares7.13																			

Masslak Implementation Timeline


Planned task Already built in the repository Milestone Ramadan and Eid (approximate) Today

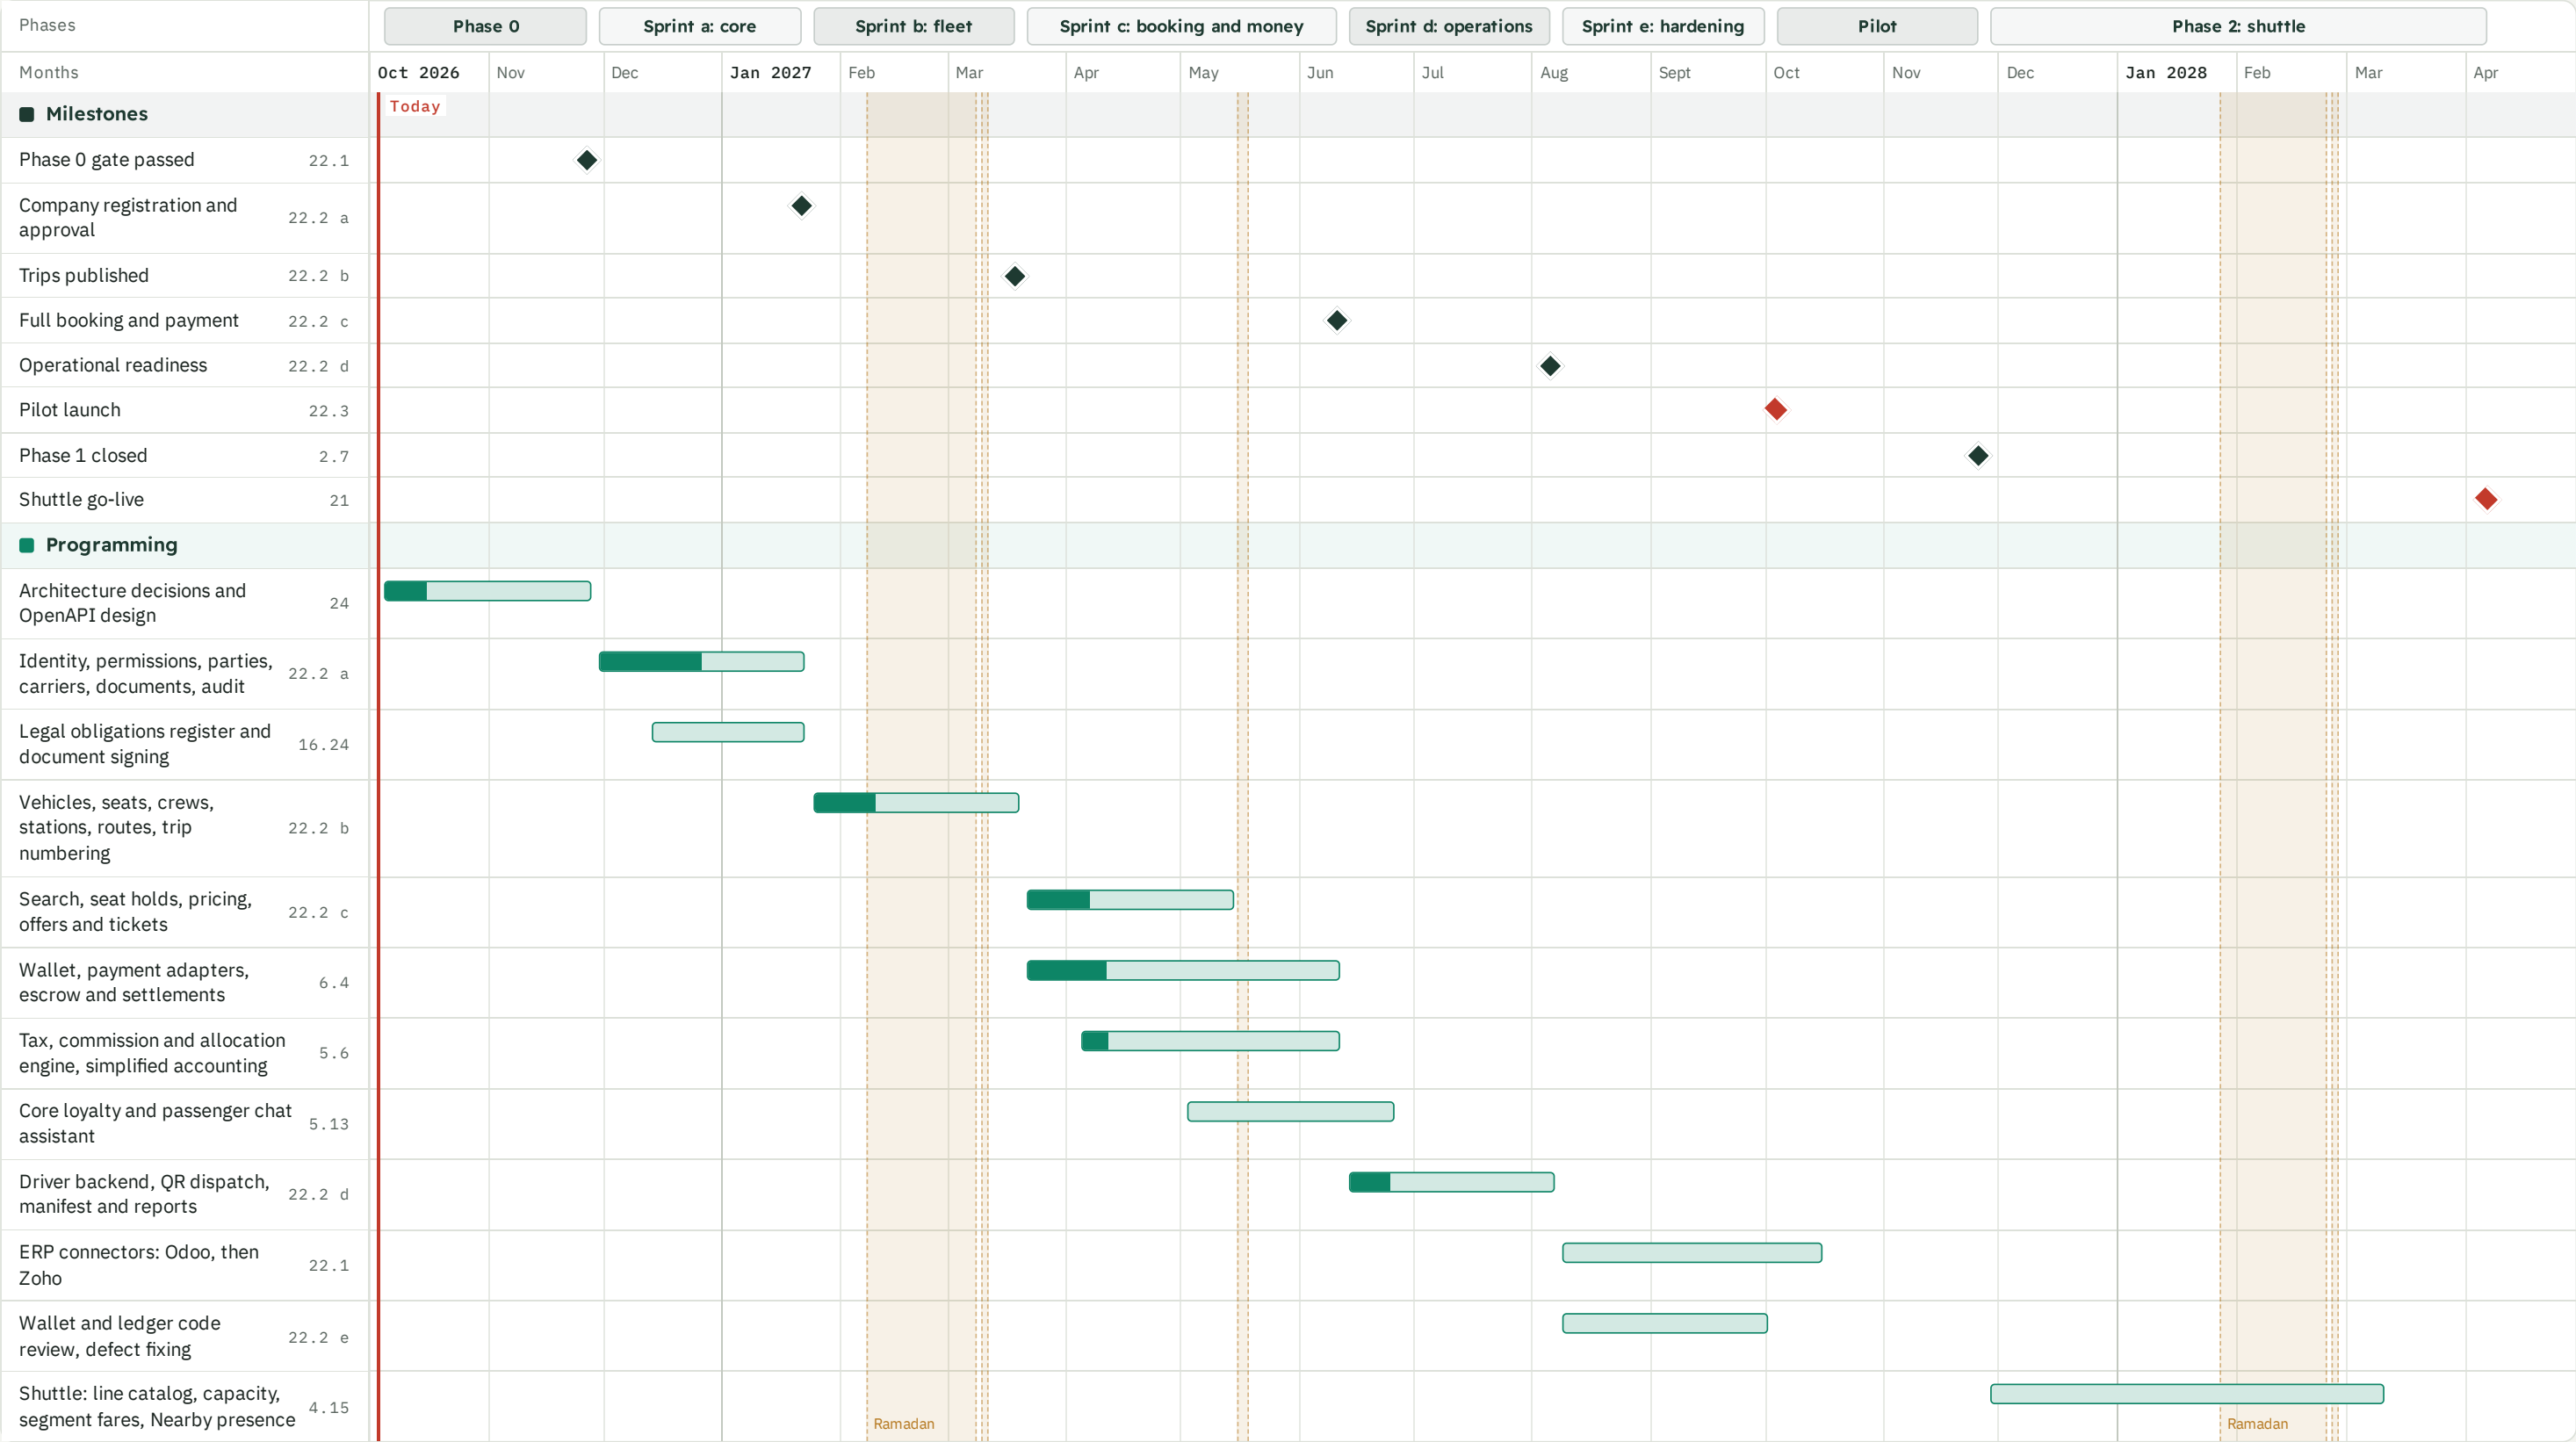

Source: Analysis and Design Study v2.5, sections 20.4, 21 and 22, and the repository contents as of 3 October 2026. Version 1.0.

Masslak Implementation Timeline


Planned task Already built in the repository Milestone Ramadan and Eid (approximate) Today

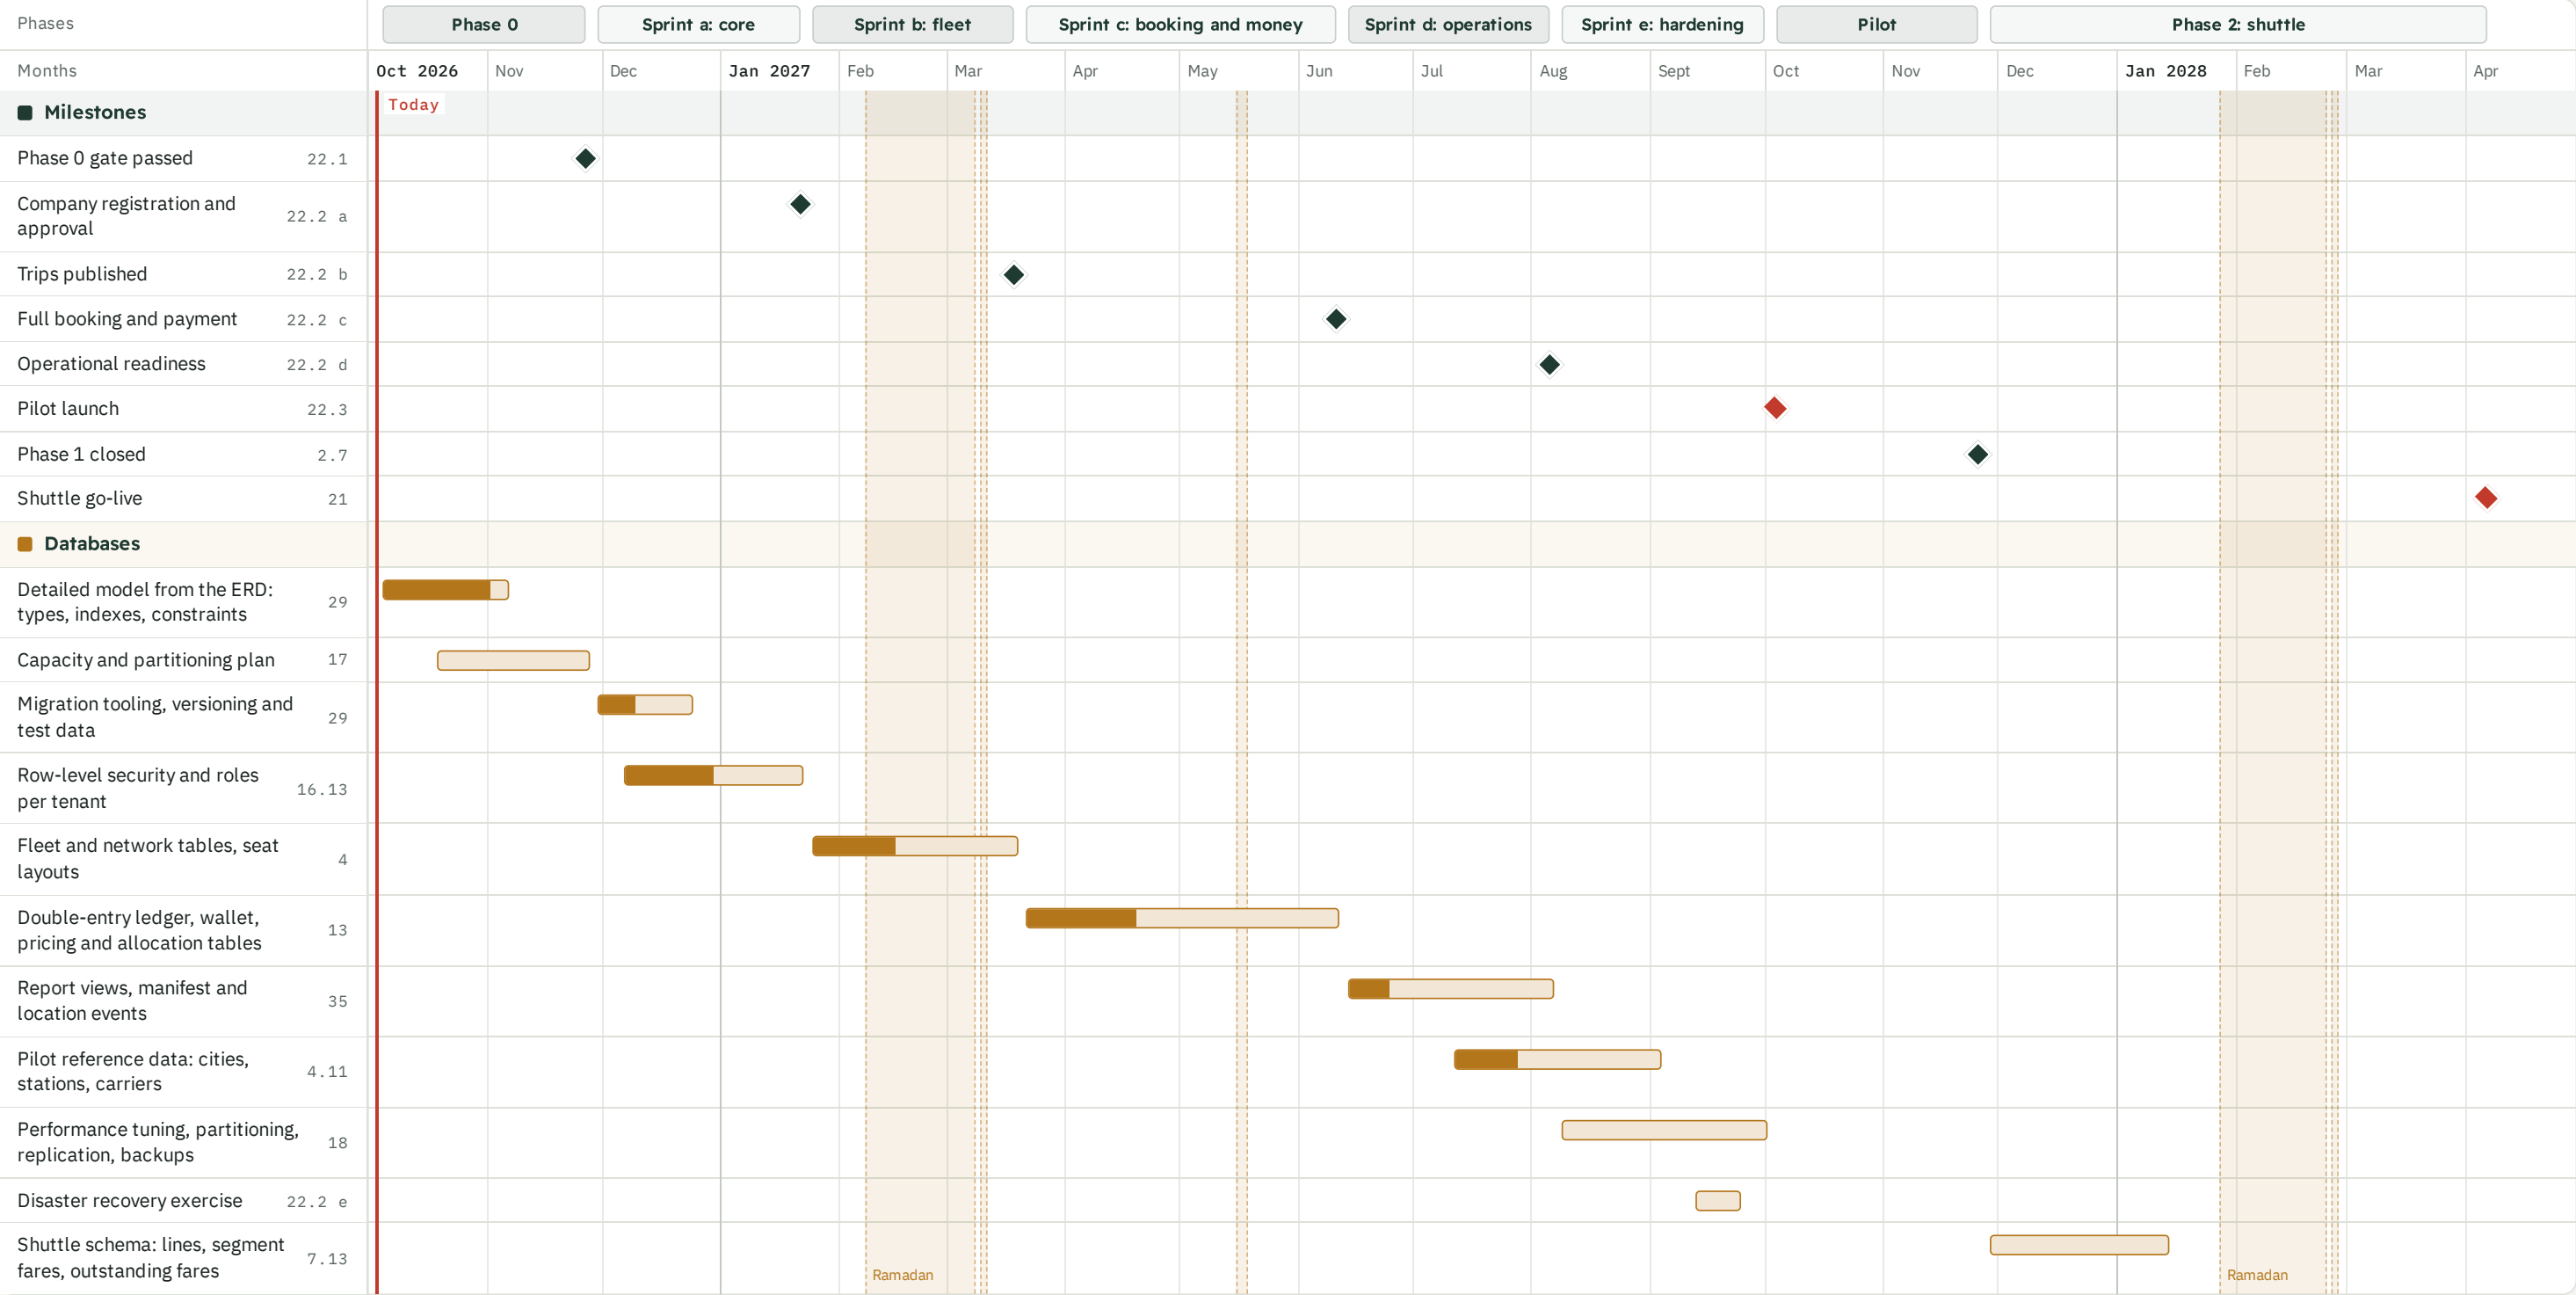

Source: Analysis and Design Study v2.5, sections 20.4, 21 and 22, and the repository contents as of 3 October 2026. Version 1.0.

Masslak Implementation Timeline


Planned task Already built in the repository Milestone Ramadan and Eid (approximate) Today

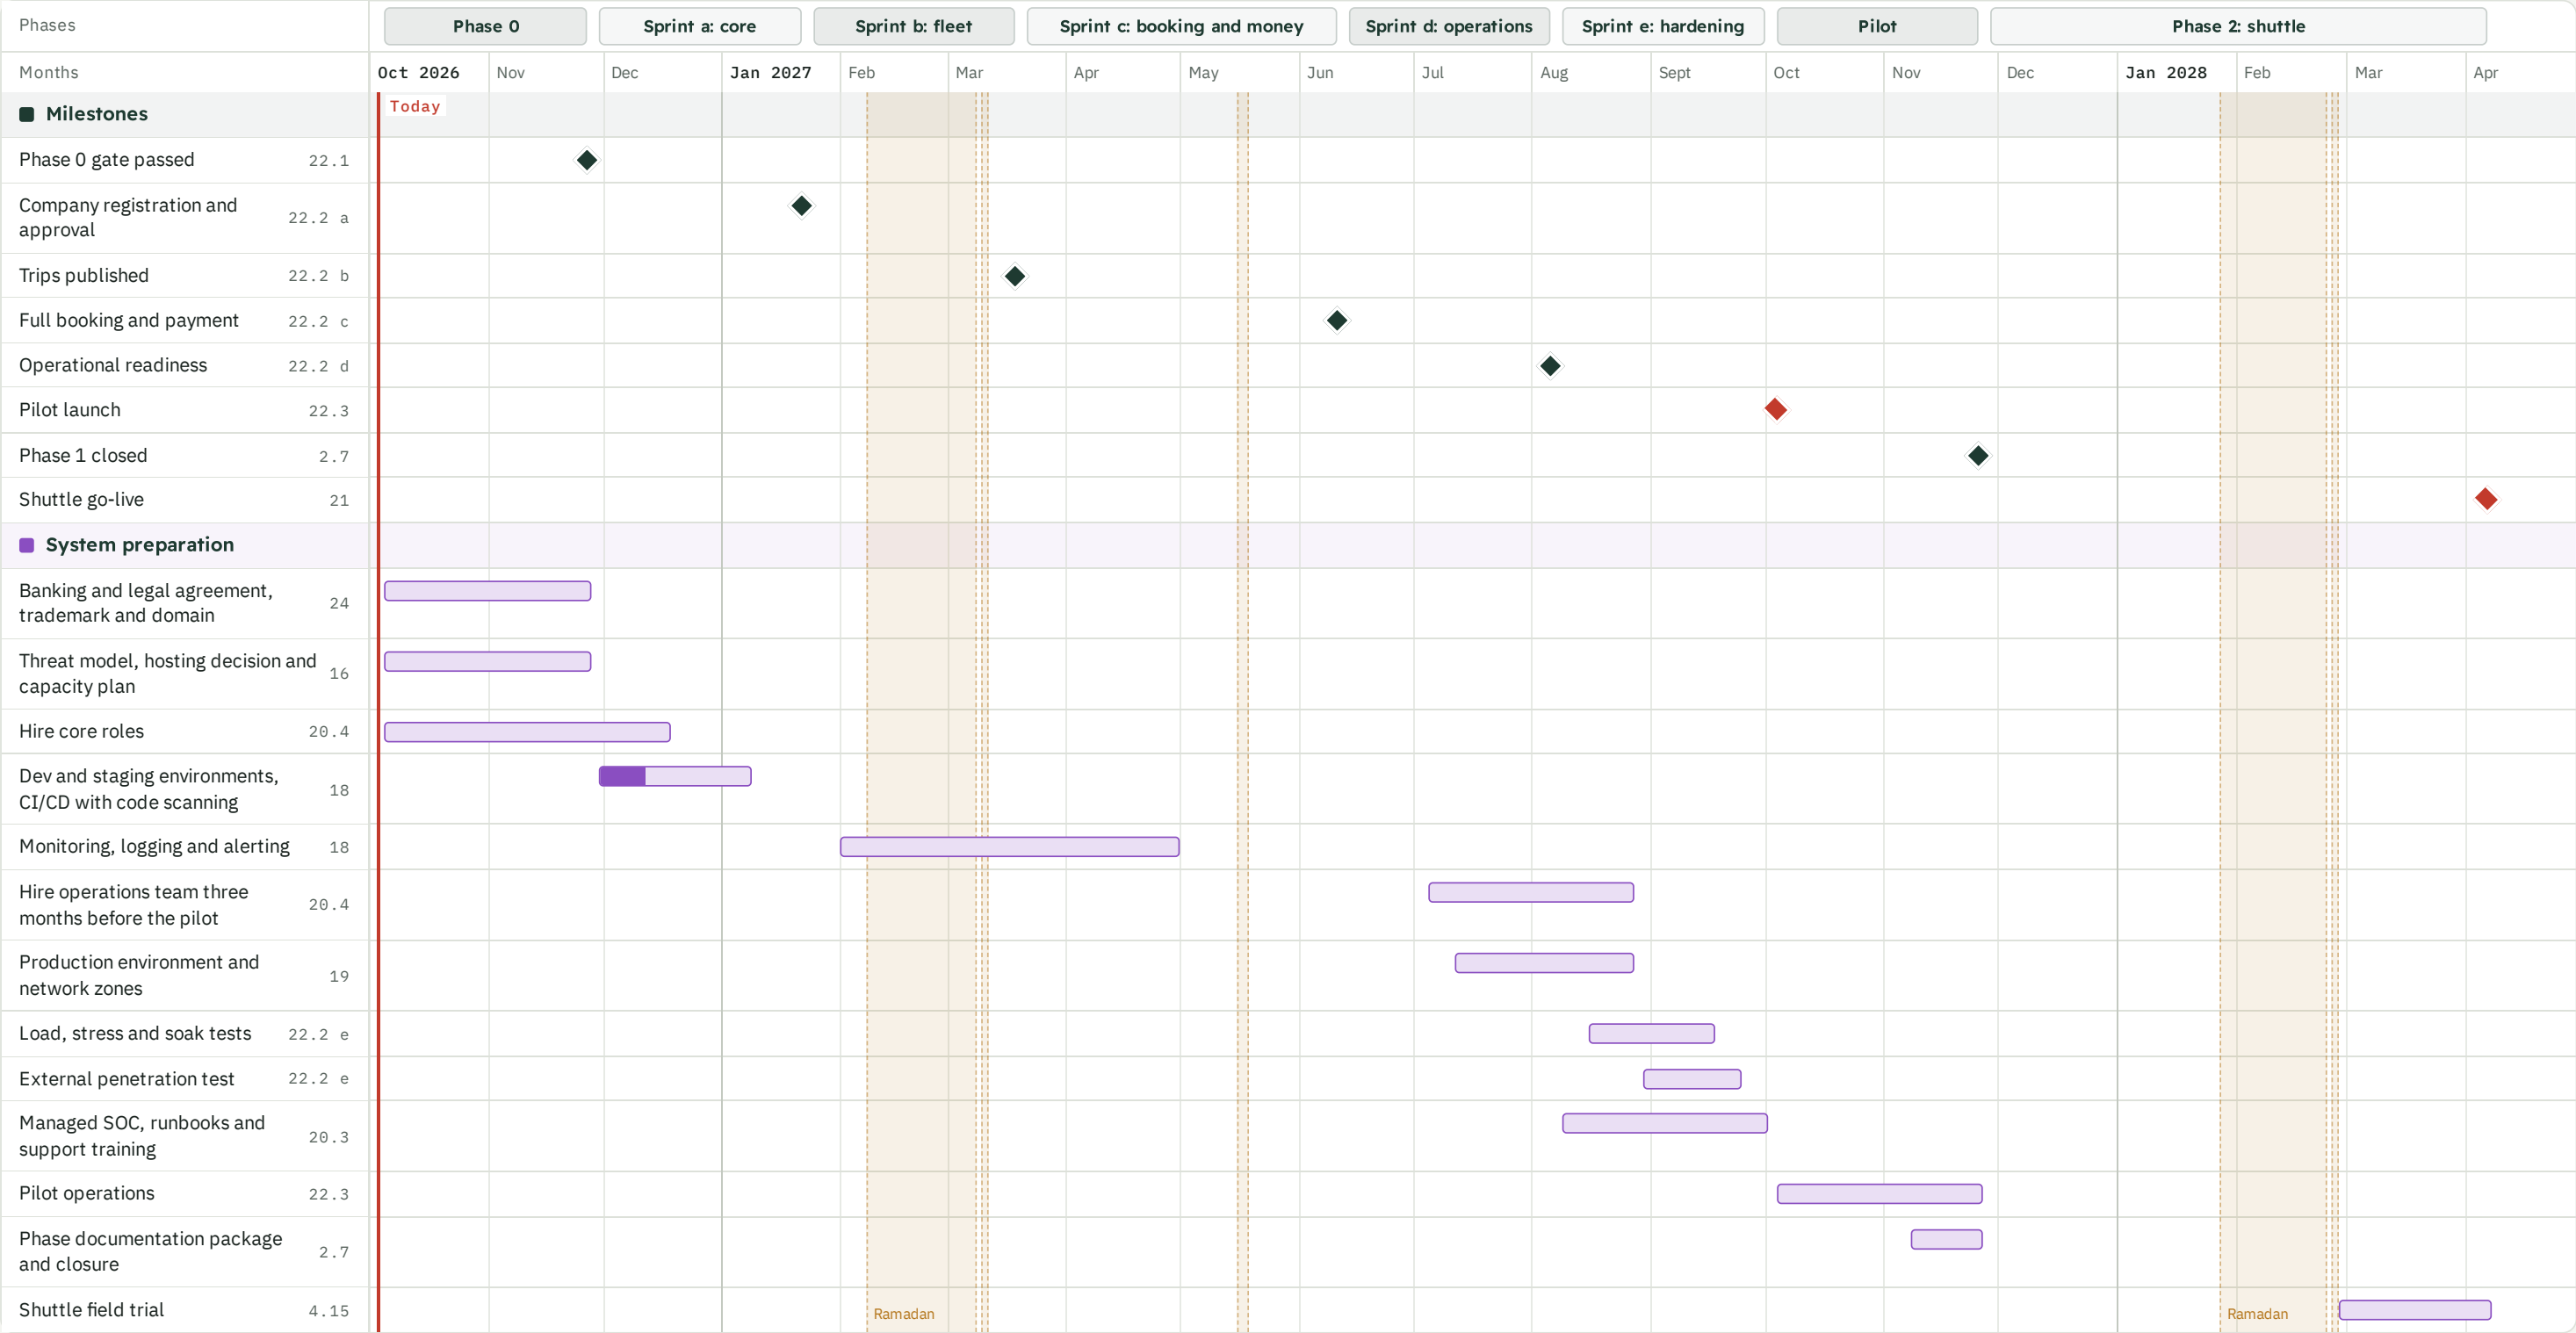

Source: Analysis and Design Study v2.5, sections 20.4, 21 and 22, and the repository contents as of 3 October 2026. Version 1.0.

Masslak Implementation Timeline

Planned task Already built in the repository Milestone Today

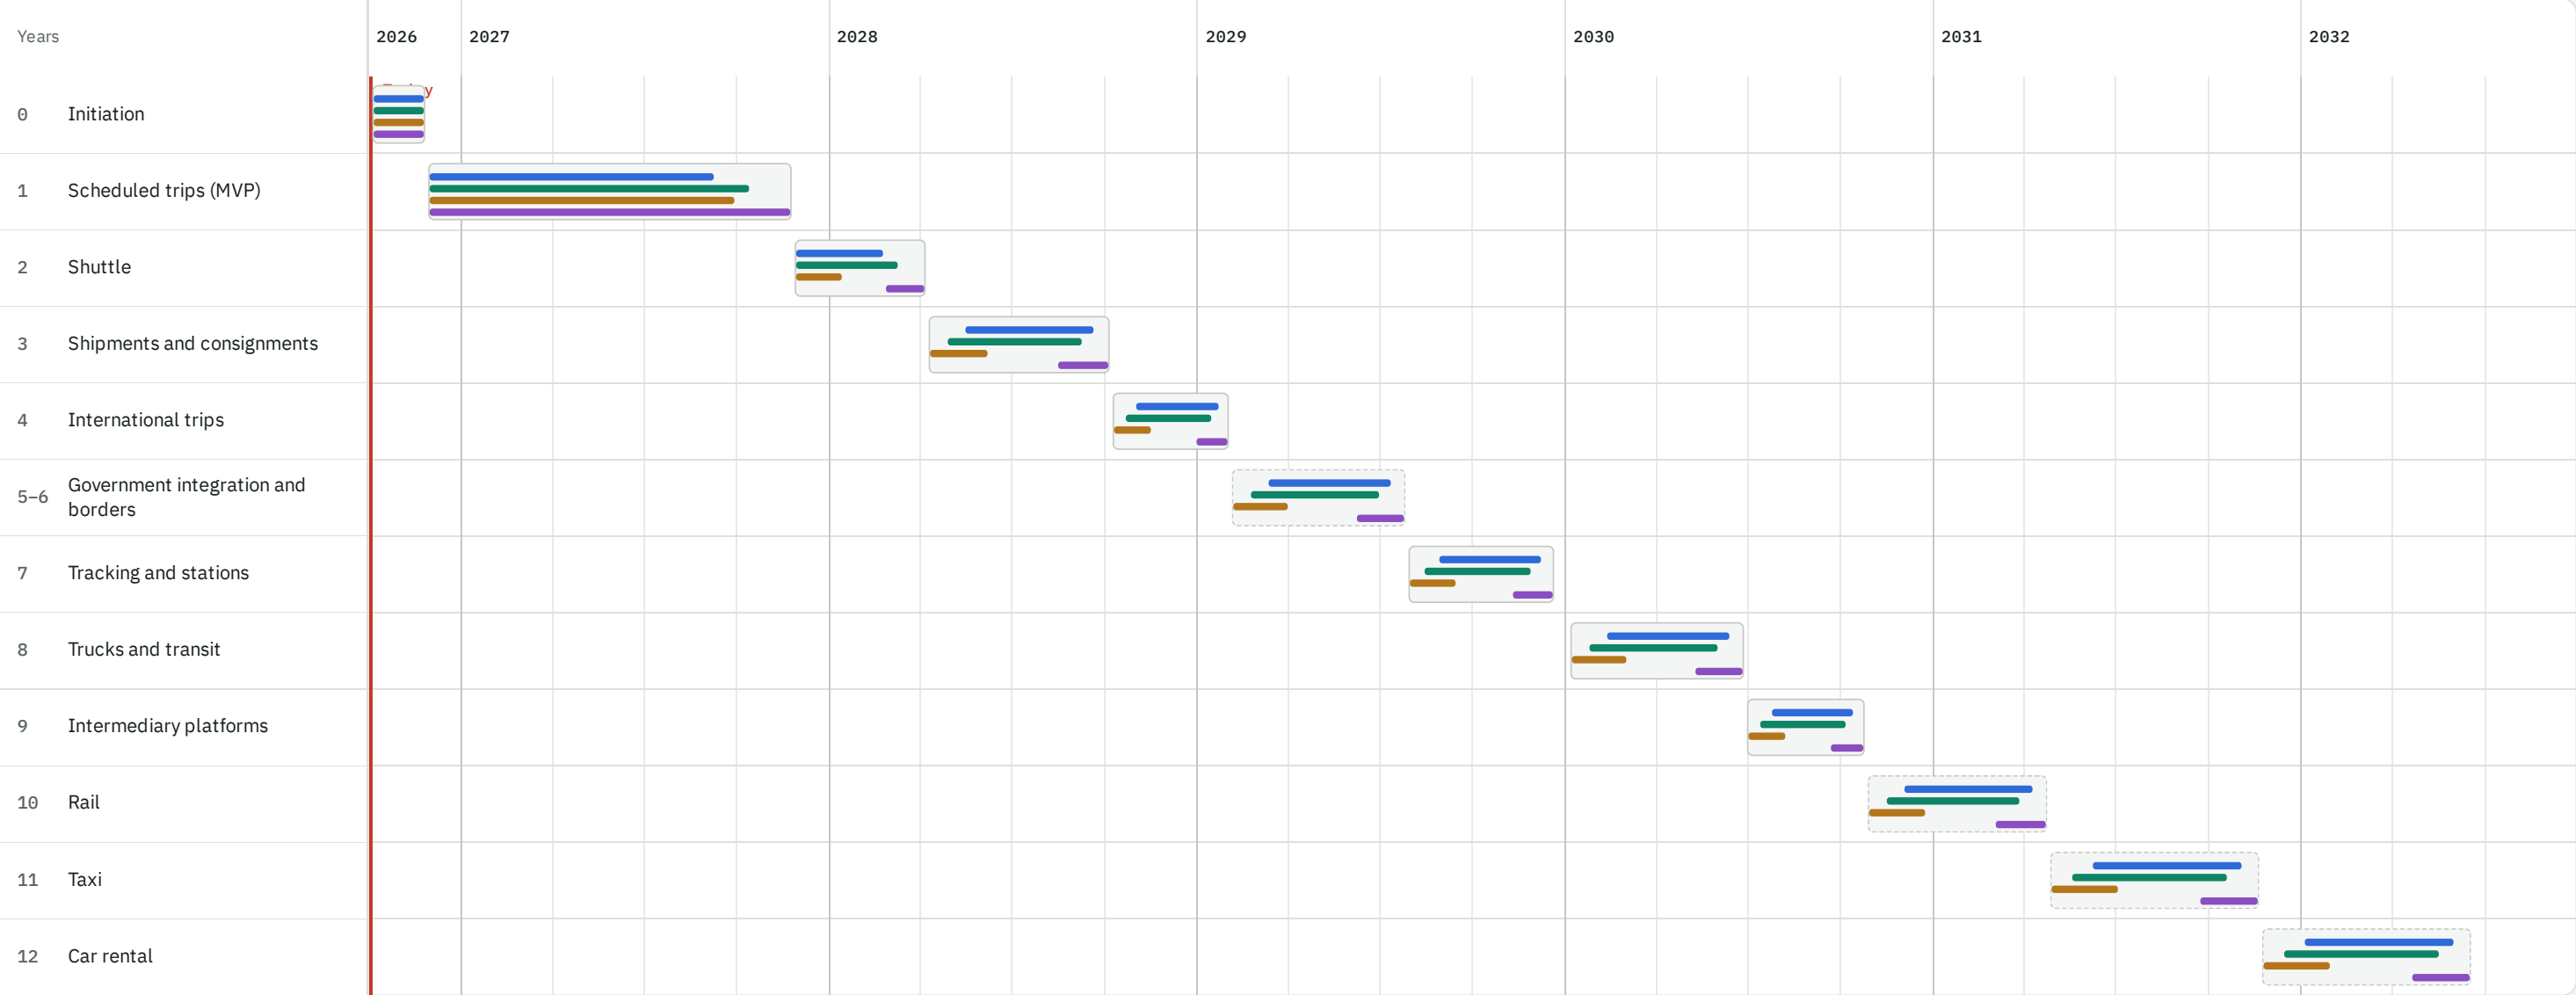

Planning assumptions

- Phase 0 starts on Monday 5 October 2026, after the study is approved and the priority decisions are resolved (section 24).
- Durations come from table 22.1, using the upper bound where a range is given: 8 weeks for Phase 0, and 12 months for Phase 1 with five sprints and a pilot launch.
- Phases run in sequence with one team. Phases 5 and 6 depend on the government authorities' readiness, so their dates may move.
- Ramadan and Eid dates are approximate because they follow the lunar calendar. The pilot launch and the shuttle field trial are placed outside them.
- Dates for Phases 10 to 12 are indicative. They start on the owner's decision, after tracking is stable and the regulator agrees.

Proposed Phase 1 team (22.3)

- A product manager, a business analyst and a solution architect.
- 4 to 5 backend developers, 2 web frontend developers, 2 mobile developers and a UX designer.
- 2 QA engineers, a DevOps engineer, a part-time security officer, and legal and financial counsel.
- Three months before the pilot: SRE and AppSec engineers, a performance engineer, L1 support, and a managed SOC (MSSP) contract (20.4).

What is already built

- The Phase 1 database schema, in English only (16 migrations up to version 1.2.0), with row-level security and reference data.
- A backend API covering booking, wallet, carrier, driver, admin, security, regulator and verification, with end-to-end tests.
- An Arabic RTL and English web interface, and a deployment stack (Docker and Caddy).
- The solid part of each bar marks this work. Durations were not shortened for it: it still needs review and hardening, and the head start becomes schedule buffer.
