


Masslak Implementation Timeline

Interfaces, programming, databases and system preparation from Phase 0 to launch, based on sections 20 to 22 of the Analysis and Design Study v2.5. Work starts on Monday 5 October 2026.

العربية

English

End of Phase 0 November 2026 Friday 27	Pilot launch October 2027 Monday 4	Phase 1 closed November 2027 Friday 26	Shuttle go-live April 2028 Friday 7
---	---	---	--

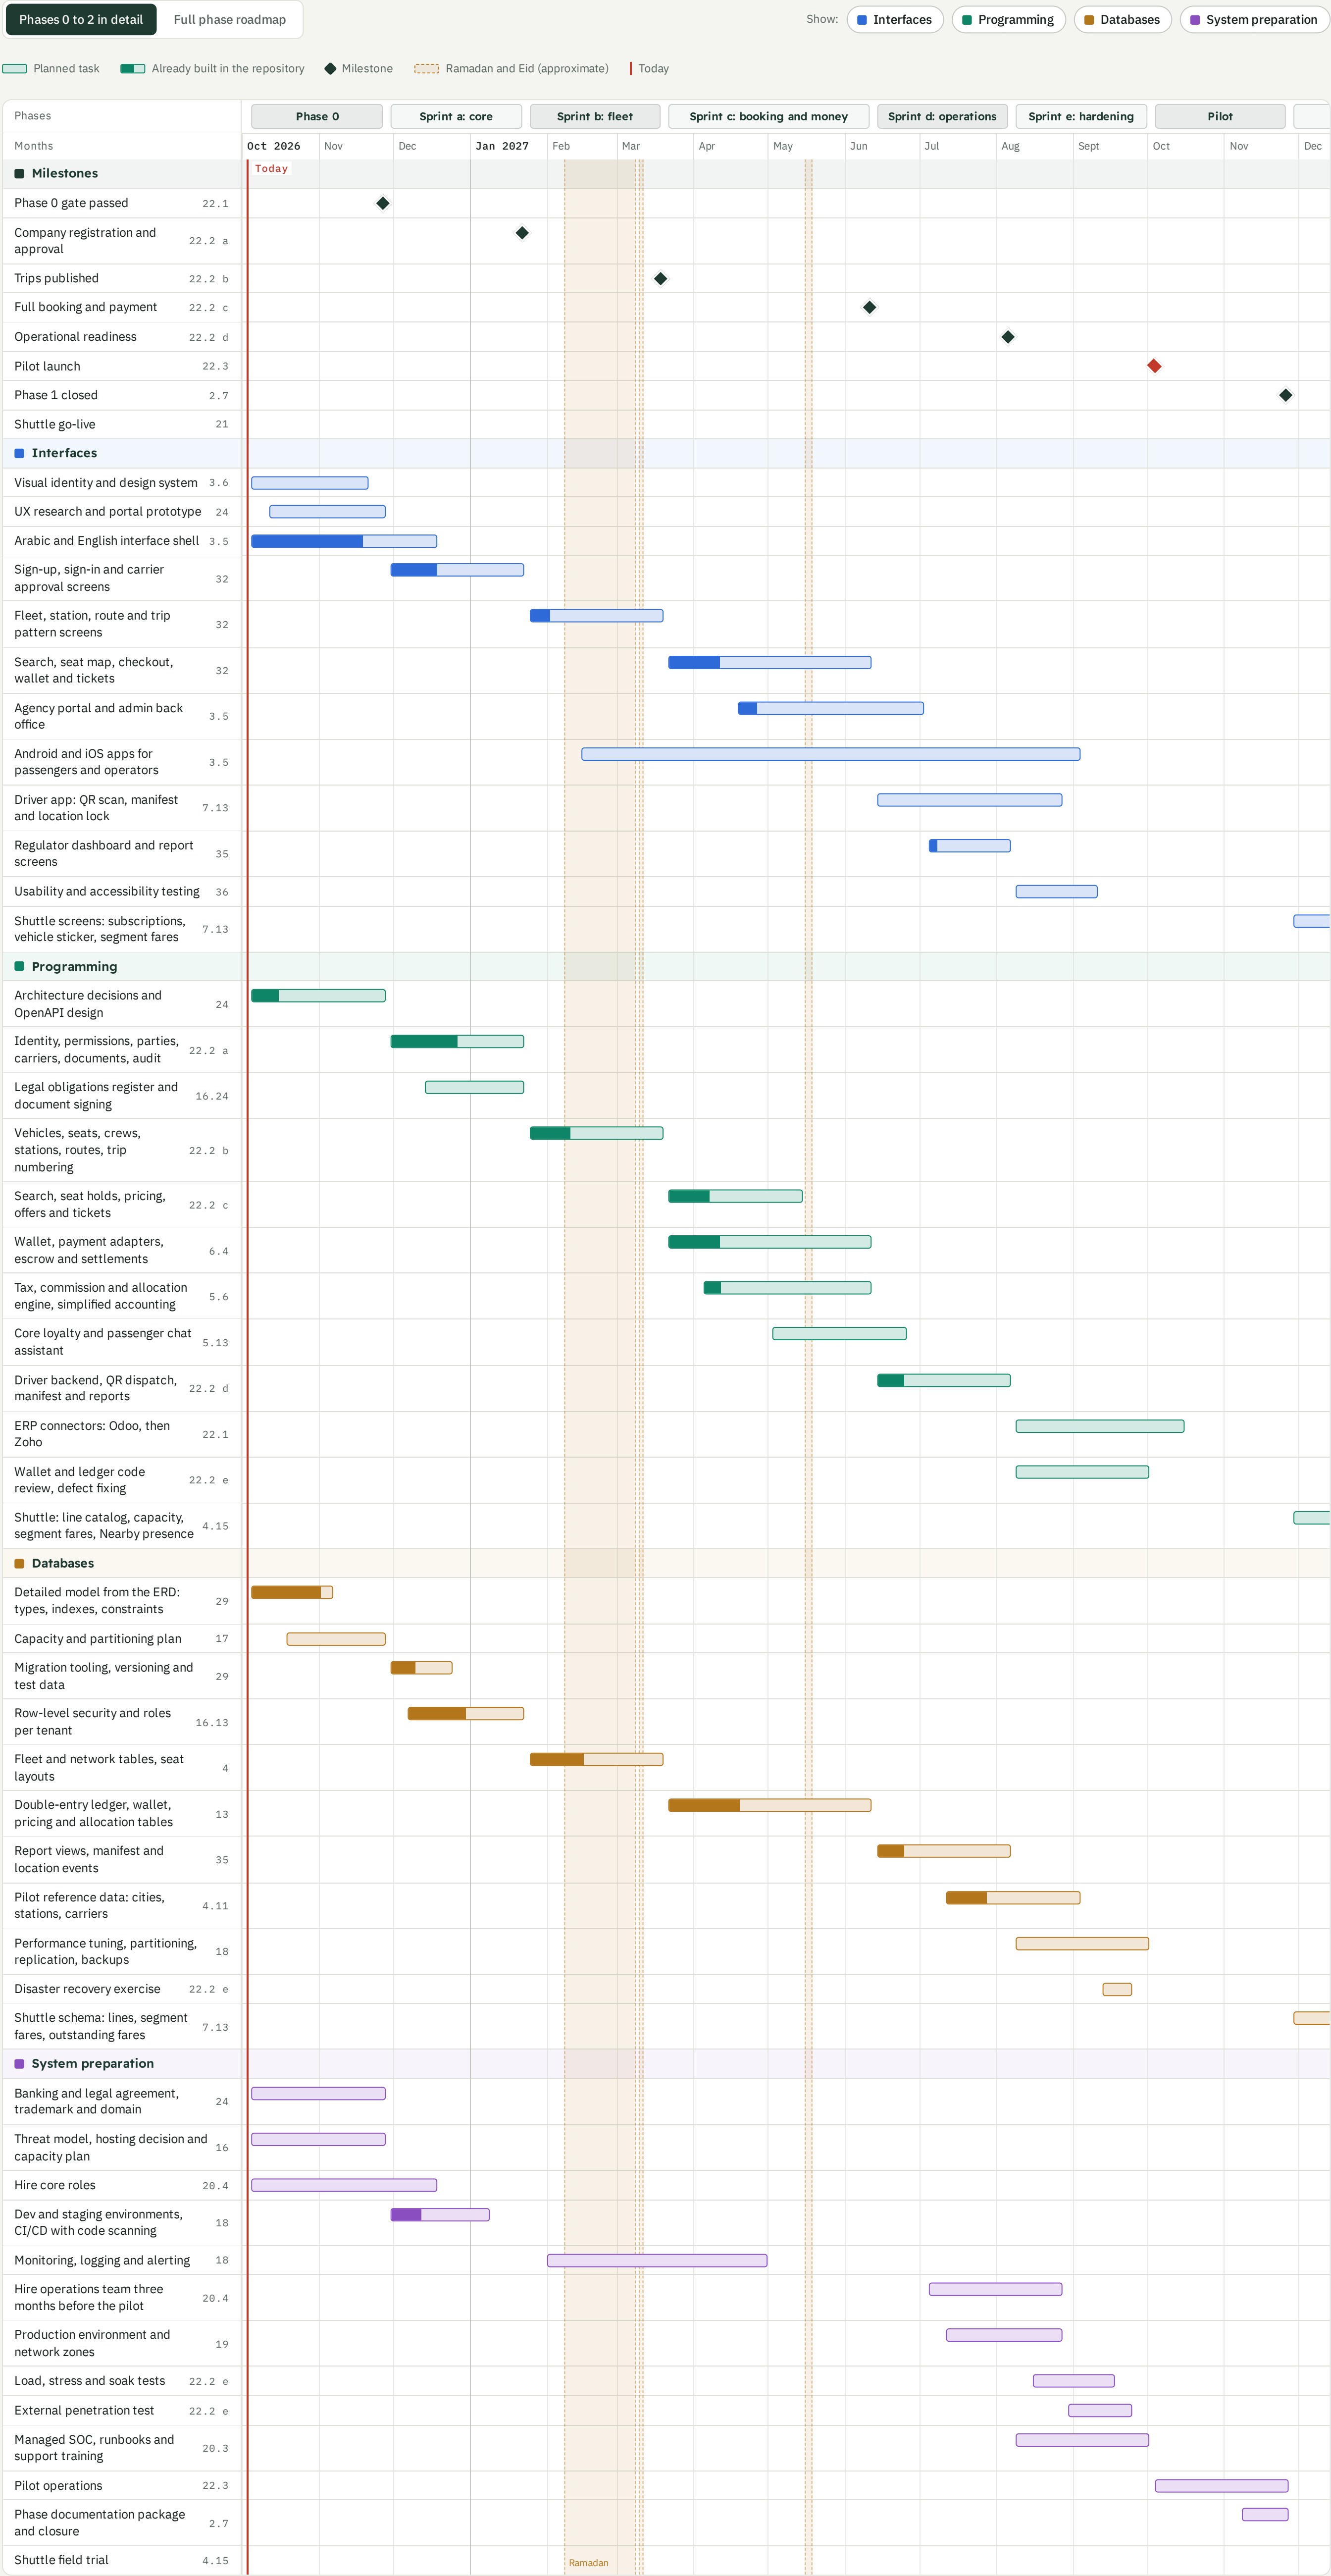

Planning assumptions

- Phase 0 starts on Monday 5 October 2026, after the study is approved and the priority decisions are resolved (section 24).
- Durations come from table 22.1, using the upper bound where a range is given: 8 weeks for Phase 0, and 12 months for Phase 1 with five sprints and a pilot launch.
- Phases run in sequence with one team. Phases 5 and 6 depend on the government authorities' readiness, so their dates may move.
- Ramadan and Eid dates are approximate because they follow the lunar calendar. The pilot launch and the shuttle field trial are placed outside them.
- Dates for Phases 10 to 12 are indicative. They start on the owner's decision, after tracking is stable and the regulator agrees.

Proposed Phase 1 team (22.3)

- A product manager, a business analyst and a solution architect.
- 4 to 5 backend developers, 2 web frontend developers, 2 mobile developers and a UX designer.
- 2 QA engineers, a DevOps engineer, a part-time security officer, and legal and financial counsel.
- Three months before the pilot: SRE and AppSec engineers, a performance engineer, L1 support, and a managed SOC (MSSP) contract (20.4).

What is already built

- The Phase 1 database schema, in English only (16 migrations up to version 1.2.0), with row-level security and reference data.
- A backend API covering booking, wallet, carrier, driver, admin, security, regulator and verification, with end-to-end tests.
- An Arabic RTL and English web interface, and a deployment stack (Docker and Caddy).
- The solid part of each bar marks this work. Durations were not shortened for it: it still needs review and hardening, and the head start becomes schedule buffer.

Masslak Implementation Timeline

Interfaces, programming, databases and system preparation from Phase 0 to launch, based on sections 20 to 22 of the Analysis and Design Study v2.5. Work starts on Monday 5 October 2026.


العربيةEnglish

End of Phase 0 November 2026 Friday 27	Pilot launch October 2027 Monday 4	Phase 1 closed November 2027 Friday 26	Shuttle go-live April 2028 Friday 7
---	---	---	--

Phases 0 to 2 in detailFull phase roadmap

Show: InterfacesProgrammingDatabasesSystem preparation

Planned taskAlready built in the repositoryMilestoneToday

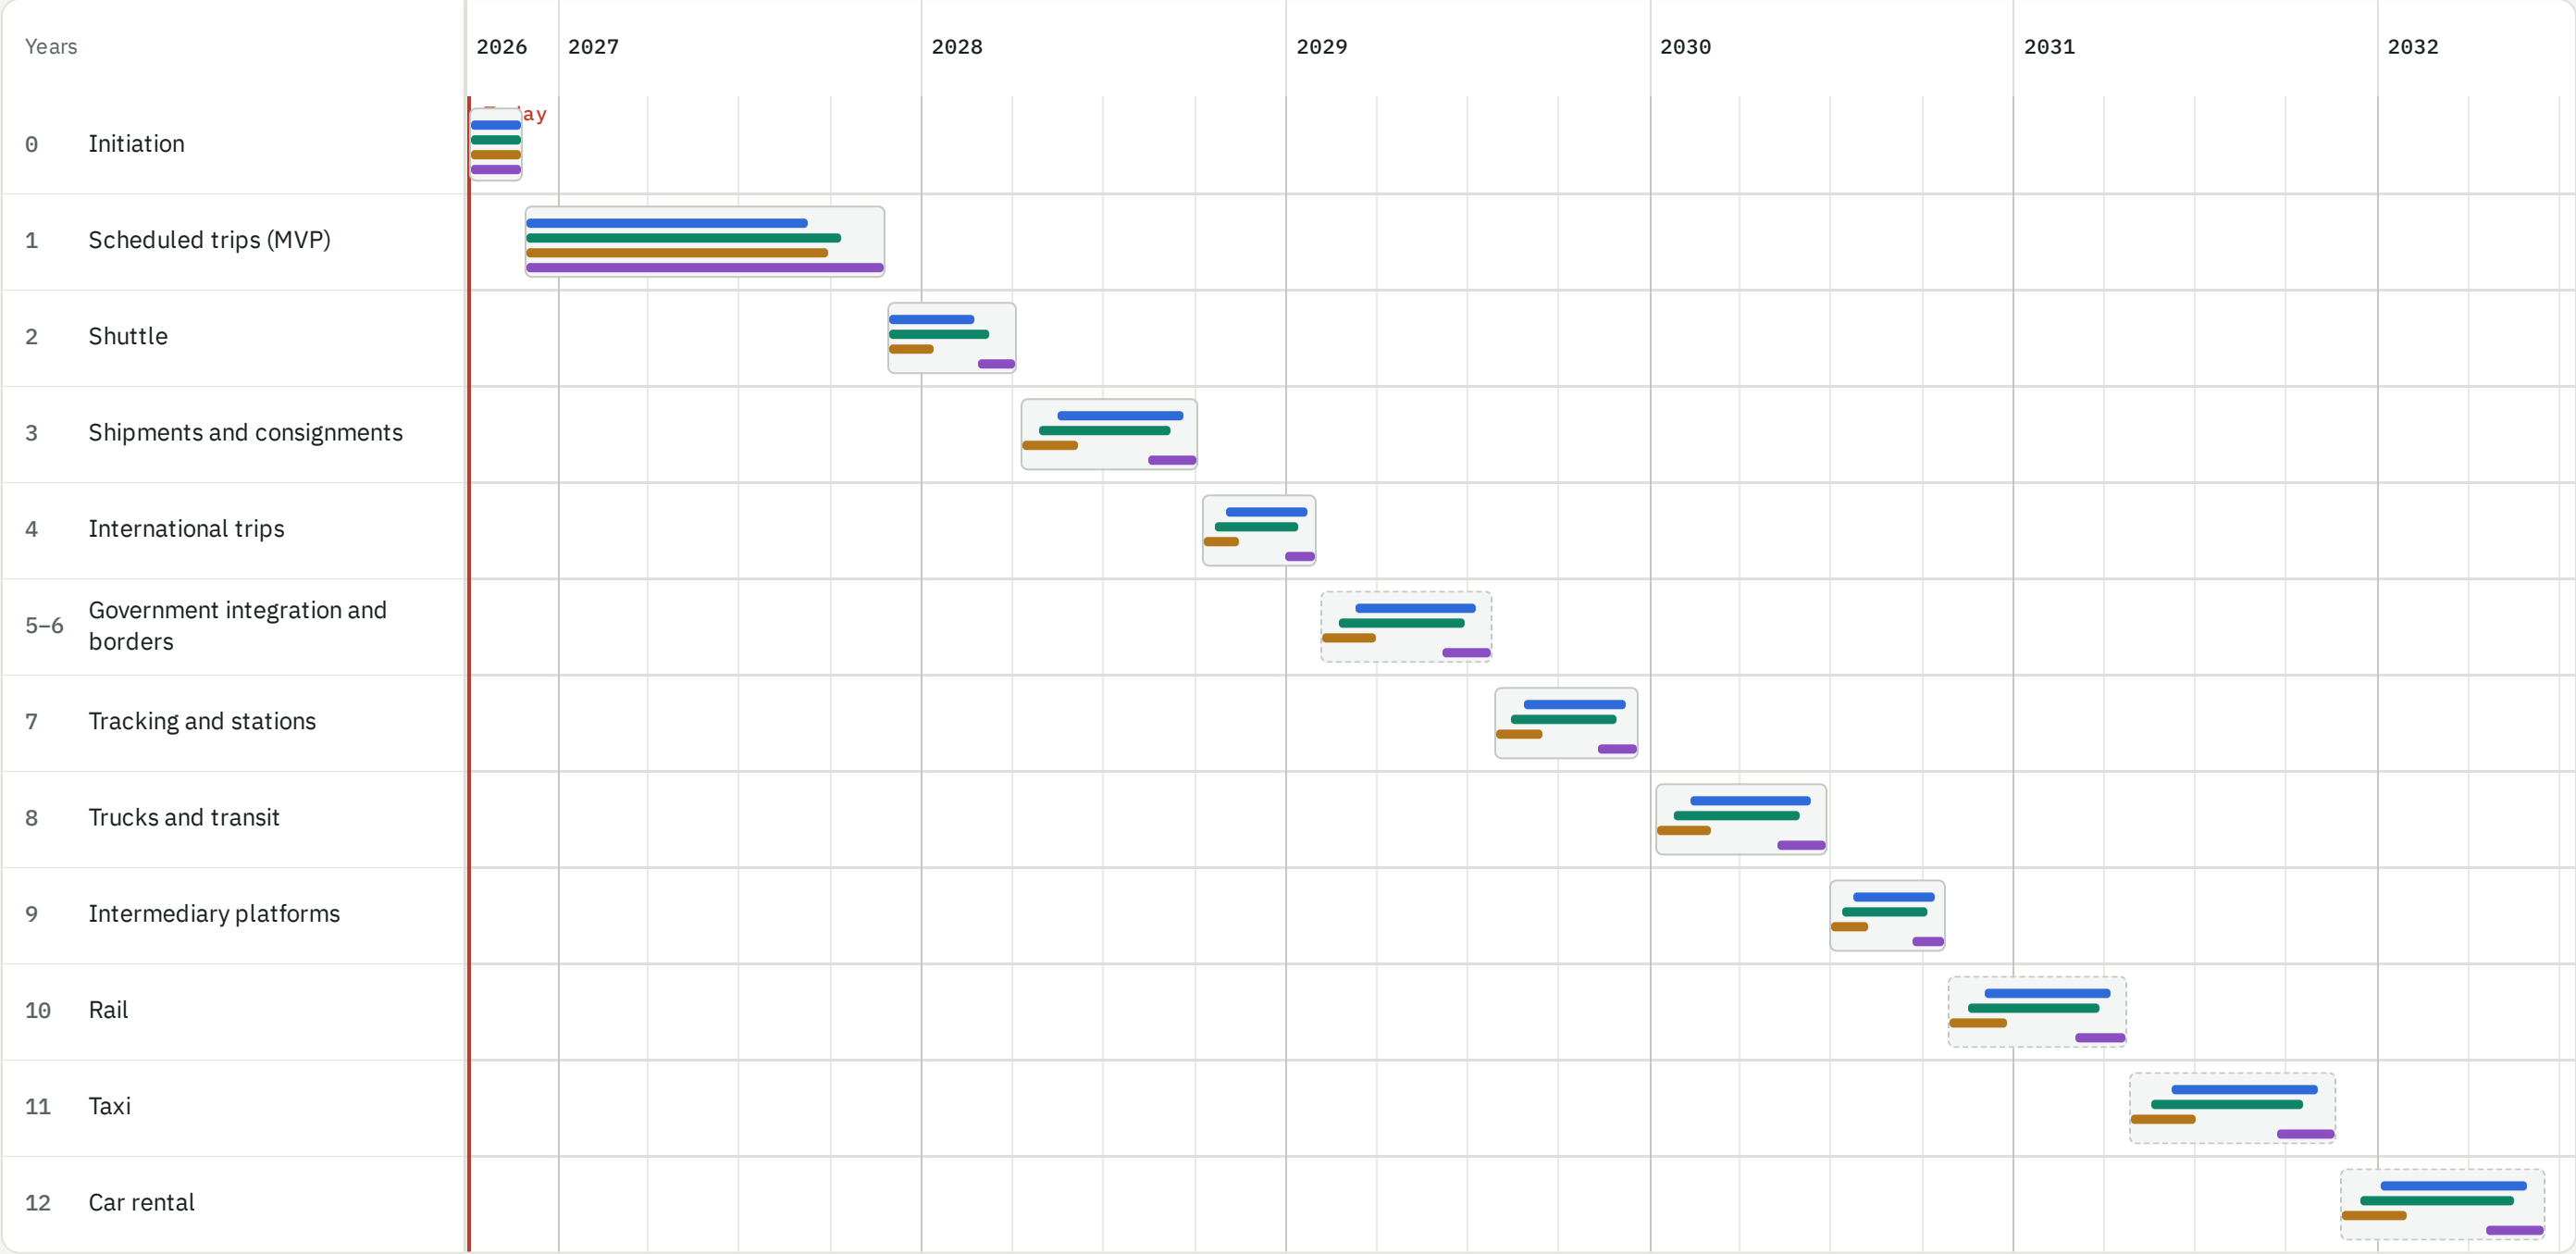

Planning assumptions

- Phase 0 starts on Monday 5 October 2026, after the study is approved and the priority decisions are resolved (section 24).
- Durations come from table 22.1, using the upper bound where a range is given: 8 weeks for Phase 0, and 12 months for Phase 1 with five sprints and a pilot launch.
- Phases run in sequence with one team. Phases 5 and 6 depend on the government authorities' readiness, so their dates may move.
- Ramadan and Eid dates are approximate because they follow the lunar calendar. The pilot launch and the shuttle field trial are placed outside them.
- Dates for Phases 10 to 12 are indicative. They start on the owner's decision, after tracking is stable and the regulator agrees.

Proposed Phase 1 team (22.3)

- A product manager, a business analyst and a solution architect.
- 4 to 5 backend developers, 2 web frontend developers, 2 mobile developers and a UX designer.
- 2 QA engineers, a DevOps engineer, a part-time security officer, and legal and financial counsel.
- Three months before the pilot: SRE and AppSec engineers, a performance engineer, L1 support, and a managed SOC (MSSP) contract (20.4).

What is already built

- The Phase 1 database schema, in English only (16 migrations up to version 1.2.0), with row-level security and reference data.
- A backend API covering booking, wallet, carrier, driver, admin, security, regulator and verification, with end-to-end tests.
- An Arabic RTL and English web interface, and a deployment stack (Docker and Caddy).
- The solid part of each bar marks this work. Durations were not shortened for it: it still needs review and hardening, and the head start becomes schedule buffer.
