
Masslak Implementation Timeline

What is done and what remains: from the built software to the pilot, the general launch and the later phases. Version 3.1, 17 October 2026; replaces version 3.0 of 15 October 2026.

Software of releases 1A and 1B built	Pilot launch	General launch	Shuttle go-live
October 2026	**January 2027**	**March 2027**	**September 2027**
Saturday 17	Monday 4	Monday 22	Friday 3
Version 1.0: end of the sprints, 1 October 2027	Version 1.0: 4 October 2027	Version 1.0: Phase 1 closed on 26 November 2027	Version 1.0: 7 April 2028

Planned task · Done · Depends on an outside party · Milestone · Holidays (approximate) · Today

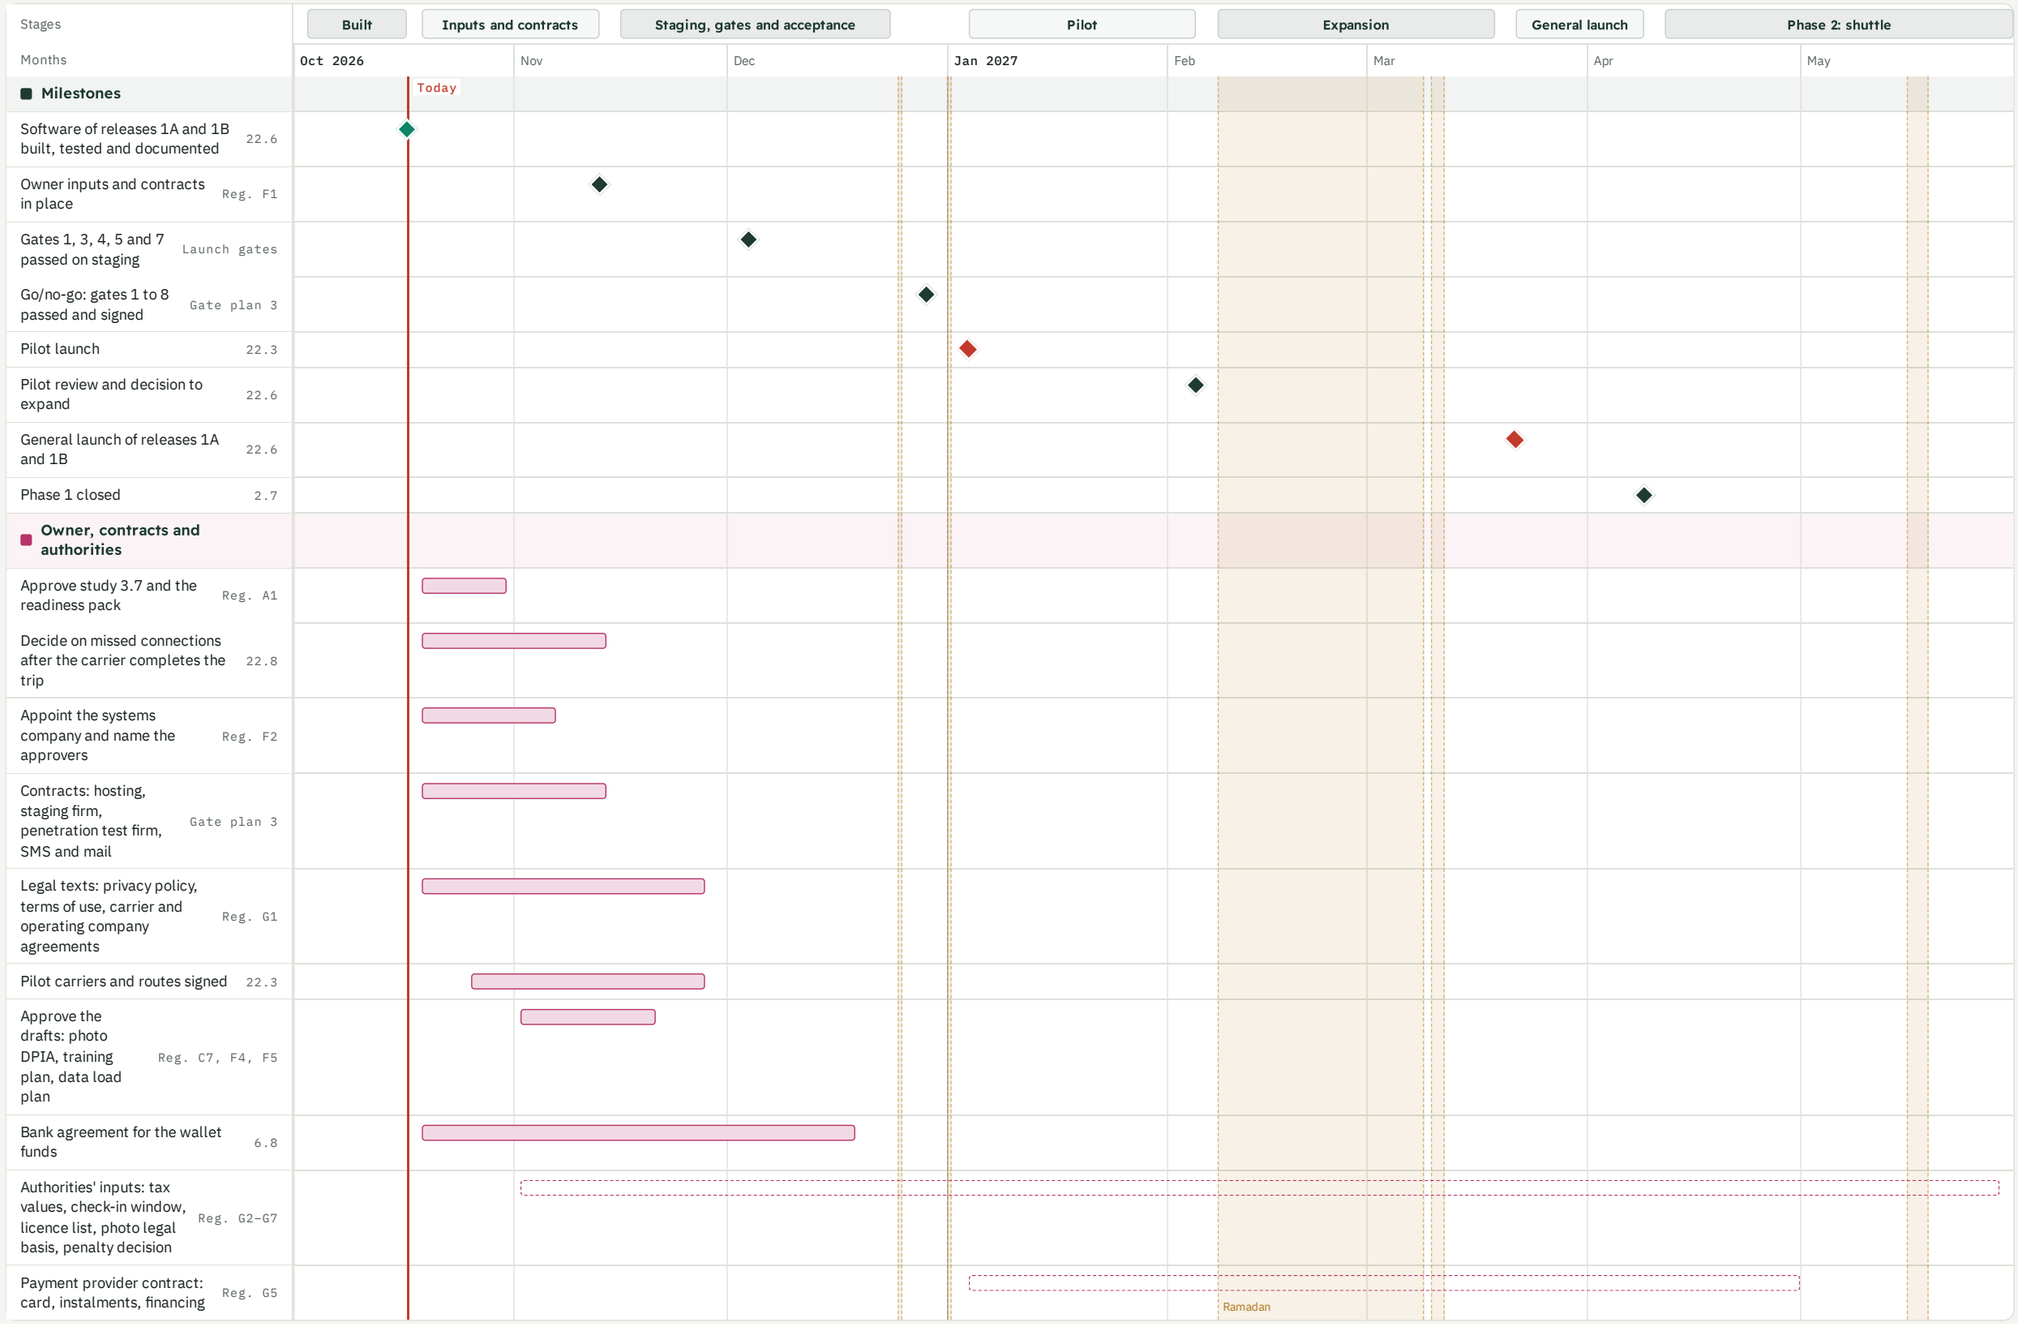

Sources: Analysis and Design Study 3.7 (sections 21, 22, 22.6, 22.7 and 22.8), the gate closure plan (docs/operations/GATE_CLOSURE_PLAN.md), the release map, the use case document 2.1 and the repository at schema file 1130, 17 October 2026. Version 3.1.

Masslak Implementation Timeline

Planned task · Done · Depends on an outside party · Milestone · Holidays (approximate) · Today

Stages	Built	Inputs and contracts	Staging, gates and acceptance	Pilot	Expansion	General launch	Phase 2: shuttle
Months	Oct 2026	Nov	Dec	Jan 2027	Feb	Mar	Apr	May
Milestones	Today							
Software of releases 1A and 1B built, tested and documented	22.6							
Owner inputs and contracts in place	Reg. F1							
Gates 1, 3, 4, 5 and 7 passed on staging	Launch gates							
Go/no-go: gates 1 to 8 passed and signed	Gate plan 3							
Pilot launch	22.3							
Pilot review and decision to expand	22.6							
General launch of releases 1A and 1B	22.6							
Phase 1 closed	2.7							
Interfaces and apps								
Web portals in Arabic and English: passenger, carrier, agency, station, finance, admin	32							
Passenger and driver apps, with offline tickets and boarding	3.10							
Station screens and the departure board	7.16							
Design review of the new screens with real users	Reg. C6							
Store accounts, app signing and the device matrix on real phones	Device matrix							
Update the Arabic user guide with the latest screens	Reg. F4							
Store review and publication of the passenger and driver apps	3.5							
Usability fixes from acceptance and the pilot	36							
Photo policy screens for the platform (API only today)	7.15				Ramadan			

Sources: Analysis and Design Study 3.7 (sections 21, 22, 22.6, 22.7 and 22.8), the gate closure plan (docs/operations/GATE_CLOSURE_PLAN.md), the release map, the use case document 2.1 and the repository at schema file 1130, 17 October 2026. Version 3.1.

Masslak Implementation Timeline

Planned task · Done · Depends on an outside party · Milestone · Holidays (approximate) · Today

Stages	Built	Inputs and contracts	Staging, gates and acceptance	Pilot	Expansion	General launch	Phase 2: shuttle
Months	Oct 2026	Nov	Dec	Jan 2027	Feb	Mar	Apr	May
Milestones								
Software of releases 1A and 1B built, tested and documented	22.6							
Owner inputs and contracts in place	Reg. F1							
Gates 1, 3, 4, 5 and 7 passed on staging	Launch gates							
Go/no-go: gates 1 to 8 passed and signed	Gate plan 3							
Pilot launch	22.3							
Pilot review and decision to expand	22.6							
General launch of releases 1A and 1B	22.6							
Phase 1 closed	2.7							
Programming								
Releases 1A and 1B: booking, wallet, cash, settlements, e-invoices, loyalty, stations	22.6							
Security: verified context, settings guard, two-step sign-in, encryption	16.42							
Since study 3.5: know your customer, regular trips, booking modes, charter, station screens, Syria's geography	3.11 to 12.7							
Connections across carriers, with the risks accepted and a booking changed to another trip	7.24							
Later phases built and switched off; partner API and reports engine	Release map							
Review of the code, requirements and traceability by the systems company	Reg. A2, A3							
Second root-detection signal: Play Integrity and App Attest	Decision 10 Oct							
Fixes from the penetration test, then the retest	Gate 8							
Pilot support: fixes and small releases	22.6							
Payment provider adapter and its sandbox tests	6.4							
Tax authority link, identity provider, booking from abroad	13.15, 3.10							

Today · Ramadan

Sources: Analysis and Design Study 3.7 (sections 21, 22, 22.6, 22.7 and 22.8), the gate closure plan (docs/operations/GATE_CLOSURE_PLAN.md), the release map, the use case document 2.1 and the repository at schema file 1130, 17 October 2026. Version 3.1.

Masslak Implementation Timeline

Planned task · Done · Depends on an outside party · Milestone · Holidays (approximate) · Today

Stages	Built	Inputs and contracts	Staging, gates and acceptance	Pilot	Expansion	General launch	Phase 2: shuttle
Months	Oct 2026	Nov	Dec	Jan 2027	Feb	Mar	Apr	May
Milestones	Today							
Software of releases 1A and 1B built, tested and documented	22.6							
Owner inputs and contracts in place	Reg. F1							
Gates 1, 3, 4, 5 and 7 passed on staging	Launch gates							
Go/no-go: gates 1 to 8 passed and signed	Gate plan 3							
Pilot launch	22.3							
Pilot review and decision to expand	22.6							
General launch of releases 1A and 1B	22.6							
Phase 1 closed	2.7							
Databases and data								
541 tables under row-level security; 143 schema files up to 1130	29							
Partitions, telemetry database, warehouse, two database hosts with failover	17.8, 16.42							
Recovery to a new host on staging	Gate 1							
Migration rehearsal at production size	Gate 4							
Production database: two hosts with a synchronous standby	16.42							
Reference data of the pilot cities: stations, counters and bays	Reg. F5							
Initial data load of the pilot carriers (bulk import)	7.17							
Audit archive bucket with object lock, and its custodian	Gate 6				Ramadan			

Sources: Analysis and Design Study 3.7 (sections 21, 22, 22.6, 22.7 and 22.8), the gate closure plan (docs/operations/GATE_CLOSURE_PLAN.md), the release map, the use case document 2.1 and the repository at schema file 1130, 17 October 2026. Version 3.1.

Masslak Implementation Timeline

Planned task · Done · Depends on an outside party · Milestone · Holidays (approximate) · Today


Stages	Months	Milestones	Software of releases 1A and 1B built, tested and documented	Owner inputs and contracts in place	Gates 1, 3, 4, 5 and 7 passed on staging	Go/no-go: gates 1 to 8 passed and signed	Pilot launch	Pilot review and decision to expand	General launch of releases 1A and 1B	Phase 1 closed	System preparation and operations	Production profile, signed images, installer, monitoring and alert rules	Launch gate tools rehearsed; readiness documents and study 3.7	On-call rota of three engineers, support and finance operations	Staging environment up	File scanning and the alert drill on staging	Capacity: 1x, 2x and 5x bursts and an 8-hour soak	External penetration test	Production environment: key service, object storage, alert receivers, egress allowlist	Training: carriers, station staff, support and finance	Acceptance tests with the owner and the pilot carriers (45 scenarios)	Egress and the audit archive on production	Pilot operations, paid in cash	Controlled expansion during Ramadan: more routes and carriers	Phase 1 documentation package and closure
Built · Inputs and contracts · Staging, gates and acceptance · Pilot · Expansion · General launch · Phase 2: shuttle	Oct 2026 · Nov · Dec · Jan 2027 · Feb · Mar · Apr · May		22.6	Reg. F1	Launch gates	Gate plan 3	22.3	22.6	22.6	2.7		16.42	Gate plan 2	Staffing	Staging	Gates 7, 5	Gate 3	Gate 8	Prod. profile	Reg. F4	Reg. D1, D5	Gates 2, 6	22.3	22.6	2.7

Today · Ramadan

Sources: Analysis and Design Study 3.7 (sections 21, 22, 22.6, 22.7 and 22.8), the gate closure plan (docs/operations/GATE_CLOSURE_PLAN.md), the release map, the use case document 2.1 and the repository at schema file 1130, 17 October 2026. Version 3.1.

Masslak Implementation Timeline

Planned task · Done · Depends on an outside party · Milestone · Today

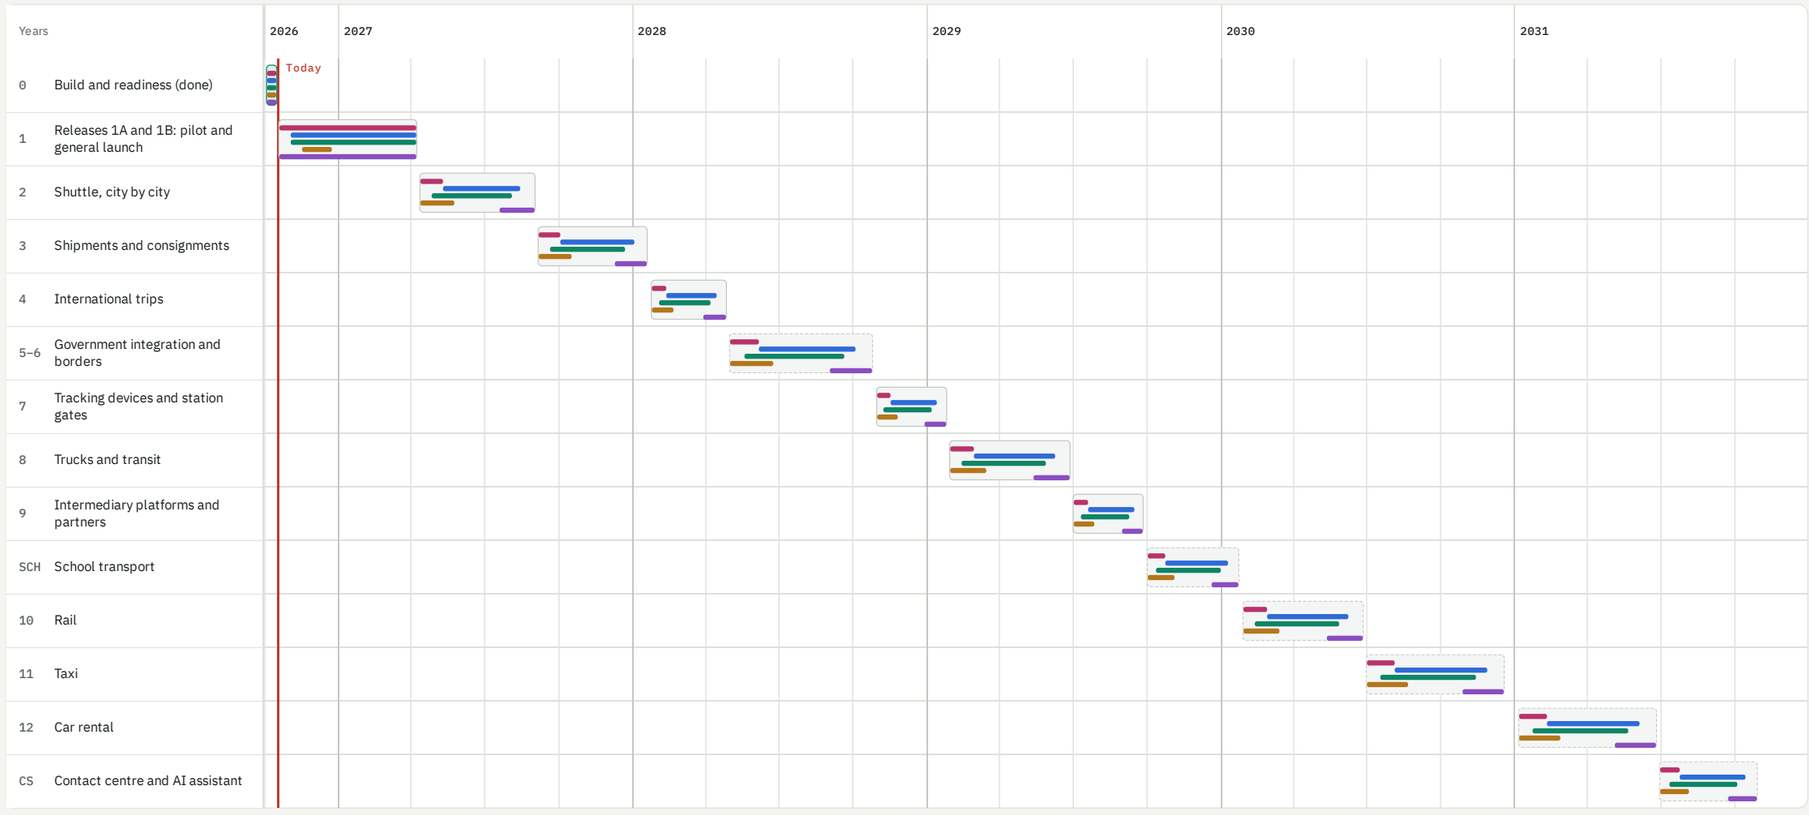

What is done (3 to 17 October 2026)

- Releases 1A and 1B are built: booking, wallet and payments with cash first, settlements, e-invoices with the tax engine, loyalty, support cases, families, manifests, and boarding stations with counter sales and the departure board.
- Web portals in Arabic and English for passengers, carriers, agencies, station operating companies, finance and administration; passenger and driver apps with offline tickets.
- The database has 143 schema files up to 1130 and 541 tables under row-level security; 867 database checks and 754 API tests pass; releases 1.48.0 to 1.50.0 are signed.
- Production readiness in the code: the production profile, two database hosts with failover, signed images, monitoring and alert rules, and the launch gate tools, rehearsed.
- Later phases are built and switched off. Of 220 use cases, 151 are built (108 on at launch, 43 off until switched on), 15 partly, 49 have data and screens only, and 5 are not built.
- Documents: study 3.7, database design 3.14, requirements, traceability, business rules, behaviour models, the test plan and the readiness register 1.9.
- Since study 3.5 (schema files 1113 to 1129): know your customer for companies, logos and four-digit trip numbers, regular trips, booking modes and groups, seats chosen on each trip, charter with a deposit, separate departures and arrivals screens paired by a short code, Syria's administrative geography with field surveys, boundaries, corrected names and a map, and the photo settings screens.
- Since study 3.6 (schema file 1130): connections across carriers where no trip runs direct (Daraa to Aleppo through Damascus), with the risks accepted, flexible later trips, each carrier's policy for a missed trip and a booking changed to another trip.

What remains before the pilot

- Owner inputs: approvals, the systems company, contracts (hosting, staging firm, penetration test, SMS and mail), legal texts and the pilot carriers.
- Evidence on staging and production for launch gates 1 to 8. Only staging or production evidence can pass a gate; the development team cannot.
- People: an on-call rota of three engineers, support and finance operations, each trained on its track.
- Data and acceptance: the pilot cities' stations and the carriers' fleets loaded, and the 45 acceptance scenarios signed.
- The apps in the stores, after the device matrix on real phones.

Planning assumptions

- The owner's inputs are in place by 13 November 2026. Every week of delay moves every later date by a week.
- If the go/no-go slips past late January 2027, the pilot moves to after Eid al-Fitr (about 22 March 2027), so that it does not start in Ramadan.
- Staging follows the gate closure plan: about three weeks once the servers, the on-call rota, the audit bucket and the penetration test firm exist.
- The pilot is paid in cash and uses the platform's own sign-in. Card payments, identity providers and the tax authority link follow their contracts and specifications; they do not hold the pilot.
- Later phases: their tables, interfaces and many screens are built and switched off. Each window covers the workflows that are still data only, the phase's acceptance gate and any field trial. One continuing team; phases that depend on authorities or contracts are indicative.
- Ramadan and Eid dates are approximate because they follow the lunar calendar.

What changed since version 1.0

- Version 1.0 planned twelve months of programming for Phase 1, with the pilot on 4 October 2027. The software of Phase 1 is now built, so the pilot moves to 4 January 2027, and Phase 1 closes on 9 April 2027 instead of 26 November 2027.
- The critical path is no longer programming. It is the owner's inputs, the staging evidence, the people and the acceptance tests.
- A lane for the owner, contracts and authorities is added. Dashed bars depend on an outside party.
- Boarding stations, counter sales and the departure board moved from Phase 7 into the first release (owner's decision, October 2026).
- The later phases start about seven months earlier, and the roadmap ends in 2031 instead of 2032.

Sources: Analysis and Design Study 3.7 (sections 21, 22, 22.6, 22.7 and 22.8), the gate closure plan (docs/operations/GATE_CLOSURE_PLAN.md), the release map, the use case document 2.1 and the repository at schema file 1130, 17 October 2026. Version 3.1.
