Masslak Implementation Timeline

What is done and what remains: from the built software to the pilot, the general launch and the later phases. Version 3.2, 18 October 2026; replaces version 3.1 of 17 October 2026.

Software of releases 1A and 1B built	Pilot launch	General launch	Shuttle go-live
October 2026	**January 2027**	**March 2027**	**September 2027**
Sunday 18	Monday 4	Monday 22	Friday 3
Version 1.0: end of the sprints, 1 October 2027	Version 1.0: 4 October 2027	Version 1.0: Phase 1 closed on 26 November 2027	Version 1.0: 7 April 2028

To the general launch in detail | Full phase roadmap

Show: Owner, contracts and authorities | Interfaces and apps | Programming | Databases and data | System preparation and operations

Planned task | Done | Depends on an outside party | Milestone | Holidays (approximate) | Today

Stages: Built | Inputs and contracts | Staging, gates and acceptance | Pilot | Expansion | General launch | Phase 2: shuttle

Months: Oct 2026 | Nov | Dec | Jan 2027 | Feb | Mar | Apr | May

Today

Milestones

- Software of releases 1A and 1B built, tested and documented — 22.6
- Owner inputs and contracts in place — Reg. F1
- Gates 1, 3, 4, 5 and 7 passed on staging — Launch gates
- Go/no-go: gates 1 to 8 passed and signed — Gate plan 3
- Pilot launch — 22.3
- Pilot review and decision to expand — 22.6
- General launch of releases 1A and 1B — 22.6
- Phase 1 closed — 2.7

Owner, contracts and authorities

- Approve study 3.8 and the readiness pack — Reg. A1
- Decide the open points of truck transport — 22.9
- Appoint the systems company and name the approvers — Reg. F2
- Contracts: hosting, staging firm, penetration test firm, SMS and mail — Gate plan 3
- Legal texts: privacy policy, terms of use, carrier and operating company agreements — Reg. G1
- Pilot carriers and routes signed — 22.3
- Approve the drafts: photo DPIA; training plan, data load plan — Reg. C7, F4, F5
- Bank agreement for the wallet funds — 6.8
- Authorities' inputs: tax values, check-in window, licence list, photo legal basis, penalty decision — Reg. G2–G7
- Payment provider contract: card, instalments, financing — Reg. G5

Interfaces and apps

- Web portals in Arabic and English: passenger, carrier, agency, station, finance, admin — 3?
- Passenger and driver apps, with offline tickets and boarding — 3.10
- Station screens and the departure board — 7.16
- Design review of the new screens with real users — Reg. C6
- One redesign of the website and apps after the documents, with the truck transport screens — 7.25
- Store accounts, app signing and the device matrix on real phones — Device matrix
- Update the Arabic user guide with the latest screens — Reg. F4
- Store review and publication of the passenger and driver apps — 3.5
- Usability fixes from acceptance and the pilot — 3б
- Photo policy screens for the platform (API only today) — 7.15

Programming

- Releases 1A and 1B: booking, wallet, cash, settlements, e-invoices, loyalty, stations — 22.6
- Security: verified context, settings guard, two-step sign-in, encryption — 16.42
- Since study 3.5: know your customer, regular trips, booking modes, charter, station screens, Syria's geography — 3.11 to 12.7
- Connections across carriers, with the risks accepted and a booking changed to another trip — 7.24
- Truck transport core: bills of lading, consignments, trucks, invoices, consignment notes and TCNs — 7.25
- A connection's missed trip held until the change window ends — 7.26
- Later phases built and switched off; partner API and reports engine — Release map
- Review of the code, requirements and traceability by the systems company — Reg. A2, A3
- Second root-detection signal: Play Integrity and App Attest — Decision 10 Oct
- Fixes from the penetration test, then the retest — Gate 8
- Pilot support: fixes and small releases — 22.6
- Payment provider adapter and its sandbox tests — 6.4
- Tax authority link, identity provider, booking from abroad — 13.15, 3.10

Databases and data

- 560 tables under row-level security; 145 schema files up to 1132 — 29
- Partitions, telemetry database, warehouse, two database hosts with failover — 17.8, 16.42
- Recovery to a new host on staging — Gate 1
- Migration rehearsal at production size — Gate 4
- Production database: two hosts with a synchronous standby — 16.42
- Reference data of the pilot cities: stations, counters and bays — Reg. F5
- Initial data load of the pilot carriers (bulk import) — 7.17
- Audit archive bucket with object lock, and its custodian — Gate 6

System preparation and operations

- Production profile, signed images, installer, monitoring and alert rules — 16.42
- Launch gate tools rehearsed; readiness documents and study 3.7 — Gate plan 2
- On-call rota of three engineers, support and finance operations — Staffing
- Staging environment up — Staging
- File scanning and the alert drill on staging — Gates 7, 9
- Capacity: 1x, 2x and 5x bursts and an 8-hour soak — Gate 3
- External penetration test — Gate 8
- Production environment: key service, object storage, alert receivers, egress allowlist — Prod. profile
- Training: carriers, station staff, support and finance — Reg. F4
- Acceptance tests with the owner and the pilot carriers (45 scenarios) — Reg. G1, D5
- Egress and the audit archive on production — Gates 2, 6
- Pilot operations, paid in cash — 22.3
- Controlled expansion during Ramadan: more routes and carriers — 22.6
- Phase 1 documentation package and closure — 2.7

Ramadan

What is done (3 to 18 October 2026)

- Releases 1A and 1B are built: booking, wallet and payments with cash first, settlements, e-invoices with the tax engine, loyalty, support cases, families, manifests, and boarding stations with counter sales and the departure board.
- Web portals in Arabic and English for passengers, carriers, agencies, station operating companies, finance and administration; passenger and driver apps with offline tickets.
- The database has 145 schema files up to 1132 and 560 tables under row-level security; 904 database checks and 758 API tests pass; releases 1.48.0 to 1.50.0 are signed.
- Production readiness in the code: the production profile, two database hosts with failover, signed images, monitoring and alert rules, and the launch gate tools, rehearsed.
- Later phases are built and switched off. Of 220 use cases, 151 are built (108 on at launch, 43 off until switched on), 15 partly, 49 have data and screens only, and 5 are not built.
- Documents: study 3.8, database design 3.14, requirements, traceability, business rules, behaviour models, the test plan and the readiness register 2.0.
- Since study 3.5 (schema files 1113 to 1129): know your customer for companies, logos and four-digit trip numbers, regular trips, booking modes and groups, seats chosen on each trip, charter with a deposit, separate departures and arrivals screens paired by a short code, Syria's administrative geography with field surveys, boundaries, corrected names and a map, and the photo settings screens.
- Since study 3.6 (schema file 1130): connections across carriers where no trip runs direct (Daraa to Aleppo through Damascus), with the risks accepted, flexible later trips, each carrier's policy for a missed trip and a booking changed to another trip.
- Since study 3.7 (schema files 1131 and 1132): the core of truck transport of goods and containers, inside Syria, to and from the port, in transit and across borders, with bills of lading, house bills and containers, consignments, the truck owner's prices, trucks and trailers, transport invoices per bill or container, and the consignment note and TCN the platform issues; and the money of a connection's missed trip held until the change window ends. The website was not changed, at the owner's request.

What remains before the pilot

- Owner inputs: approvals, the systems company, contracts (hosting, staging firm, penetration test, SMS and mail), legal texts and the pilot carriers.
- Evidence on staging and production for launch gates 1 to 8. Only staging or production evidence can pass a gate; the development team cannot.
- People: an on-call rota of three engineers, support and finance operations, each trained on its track.
- Data and acceptance: the pilot cities' stations and the carriers' fleets loaded, and the 45 acceptance scenarios signed.
- The apps in the stores, after the device matrix on real phones.

Planning assumptions

- The owner's inputs are in place by 13 November 2026. Every week of delay moves every later date by a week.
- If the go/no-go slips past late January 2027, the pilot moves to after Eid al-Fitr (about 22 March 2027), so that it does not start in Ramadan.
- Staging follows the gate closure plan: about three weeks once the servers, the on-call rota, the audit bucket and the penetration test firm exist.
- The pilot is paid in cash and uses the platform's own sign-in. Card payments, identity providers and the tax authority link follow their contracts and specifications; they do not hold the pilot.
- Later phases: their tables, interfaces and many screens are built and switched off. Each window covers the workflows that are still data only, the phase's acceptance gate and any field trial. One continuing team; phases that depend on authorities or contracts are indicative.
- Ramadan and Eid dates are approximate because they follow the lunar calendar.

What changed since version 1.0

- Version 1.0 planned twelve months of programming for Phase 1, with the pilot on 4 October 2027. The software of Phase 1 is now built, so the pilot moves to 4 January 2027, and Phase 1 closes on 9 April 2027 instead of 26 November 2027.
- The critical path is no longer programming. It is the owner's inputs, the staging evidence, the people and the acceptance tests.
- A lane for the owner, contracts and authorities is added. Dashed bars depend on an outside party.
- Boarding stations, counter sales and the departure board moved from Phase 7 into the first release (owner's decision, October 2026).
- The later phases start about seven months earlier, and the roadmap ends in 2031 instead of 2032.

Sources: Analysis and Design Study 3.8 (sections 21, 22, 22.6 to 22.9), the gate closure plan (docs/operations/GATE_CLOSURE_PLAN.md), the release map, the use case document 2.1 and the repository at schema file 1132, 18 October 2026. Version 3.2.

Masslak Implementation Timeline


What is done and what remains: from the built software to the pilot, the general launch and the later phases. Version 3.2, 18 October 2026; replaces version 3.1 of 17 October 2026.

Software of releases 1A and 1B built	Pilot launch	General launch	Shuttle go-live
October 2026	**January 2027**	**March 2027**	**September 2027**
Sunday 18	Monday 4	Monday 22	Friday 3
Version 1.0: end of the sprints, 1 October 2027	Version 1.0: 4 October 2027	Version 1.0: Phase 1 closed on 26 November 2027	Version 1.0: 7 April 2028

To the general launch in detail | **Full phase roadmap**

Show: Owner, contracts and authorities · Interfaces and apps · Programming · Databases and data · System preparation and operations

Planned task · Done · Depends on an outside party · Milestone · Today

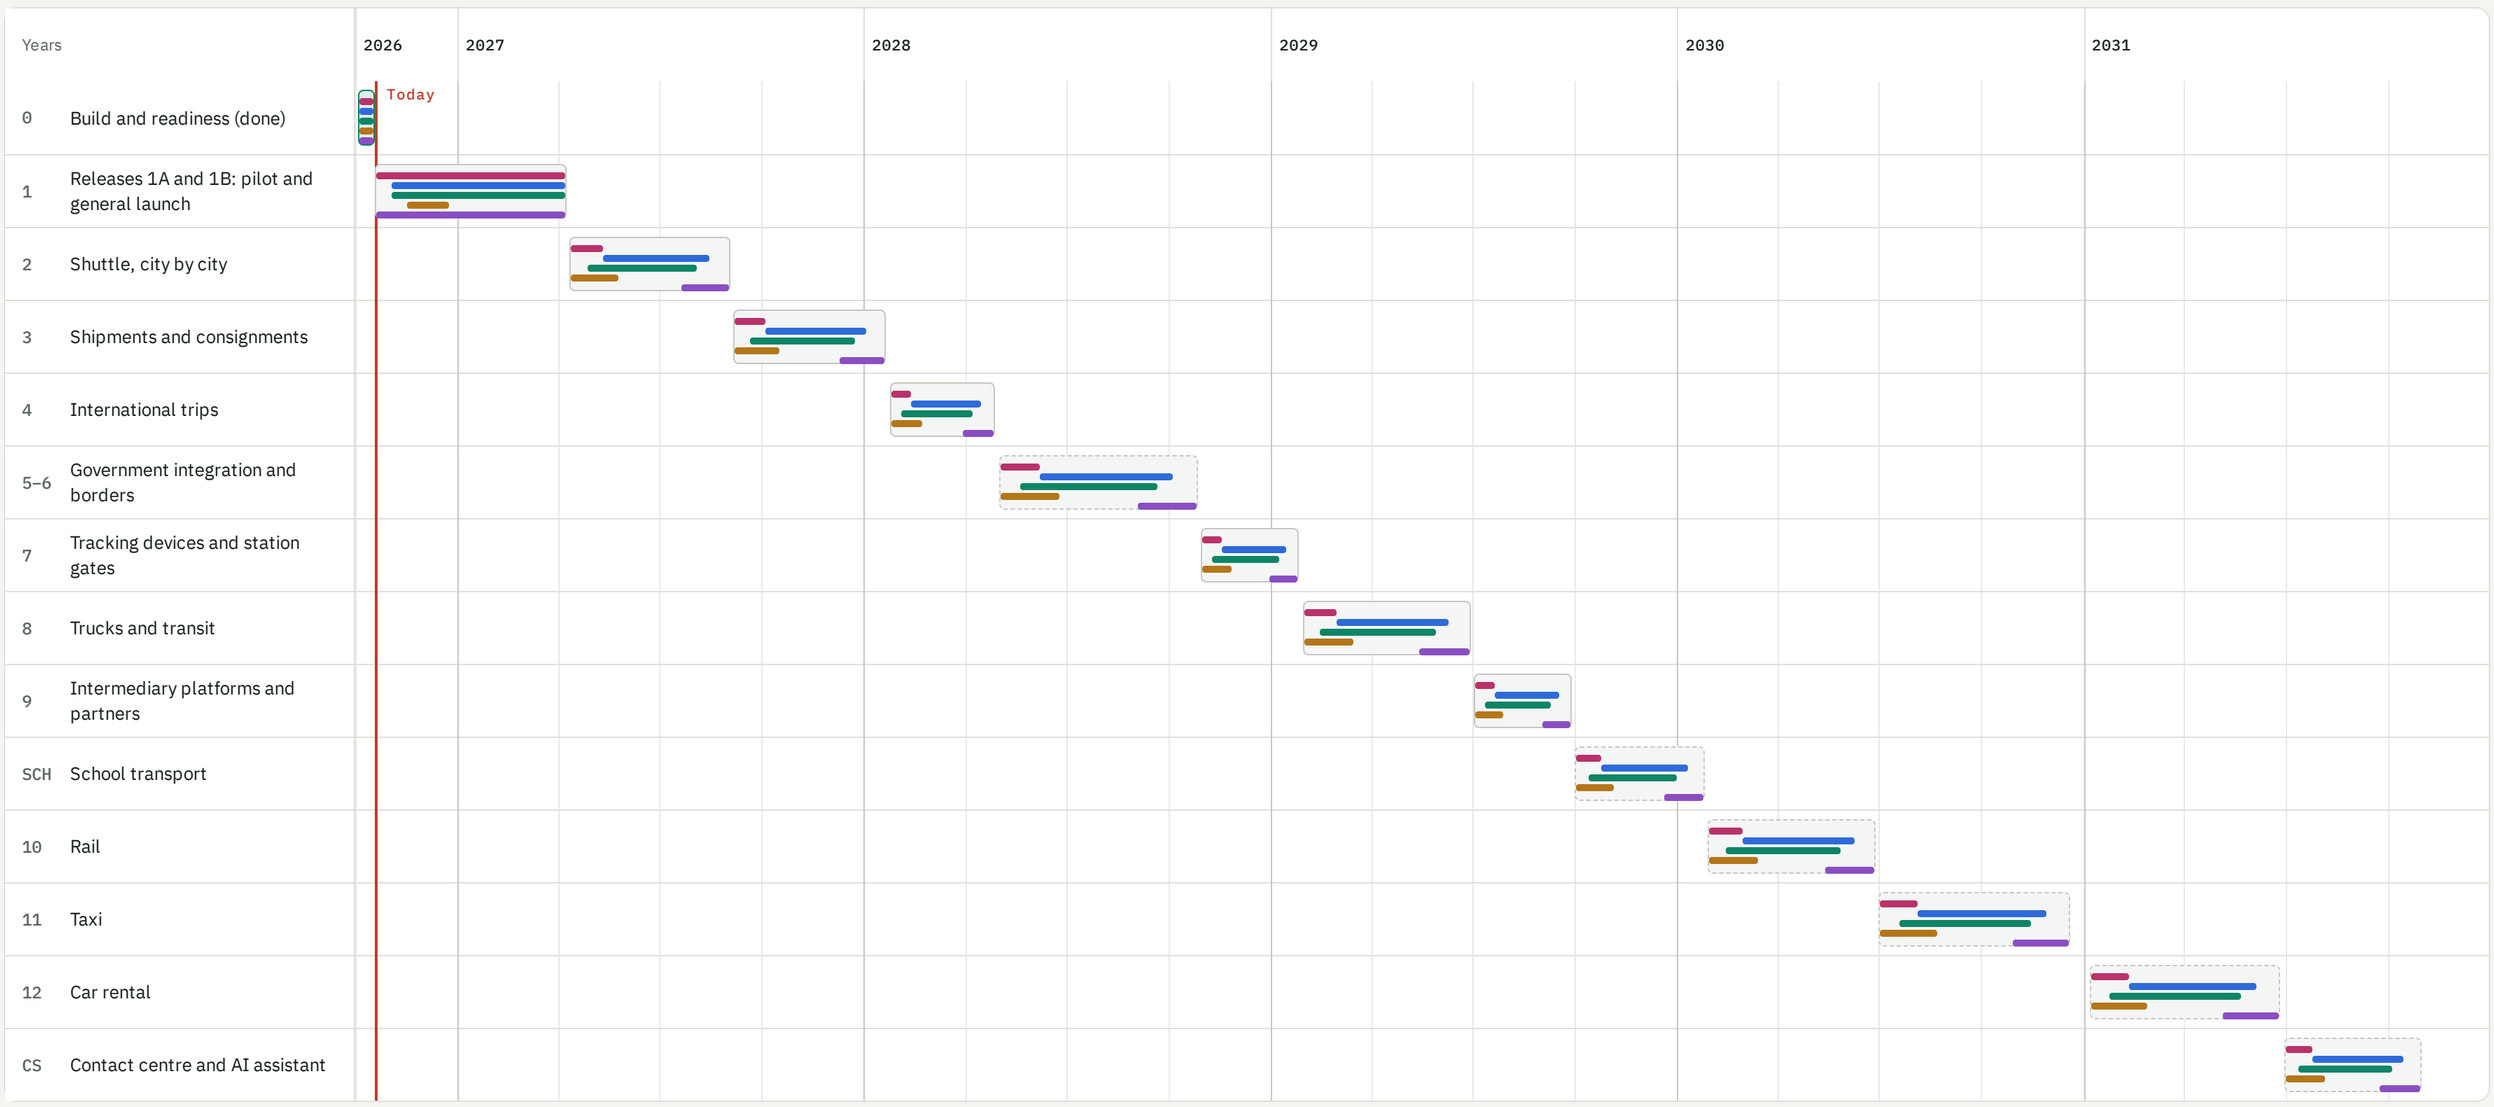

What is done (3 to 18 October 2026)

- Releases 1A and 1B are built: booking, wallet and payments with cash first, settlements, e-invoices with the tax engine, loyalty, support cases, families, manifests, and boarding stations with counter sales and the departure board.
- Web portals in Arabic and English for passengers, carriers, agencies, station operating companies, finance and administration; passenger and driver apps with offline tickets.
- The database has 145 schema files up to 1132 and 560 tables under row-level security; 904 database checks and 758 API tests pass; releases 1.48.0 to 1.50.0 are signed.
- Production readiness in the code: the production profile, two database hosts with failover, signed images, monitoring and alert rules, and the launch gate tools, rehearsed.
- Later phases are built and switched off. Of 220 use cases, 151 are built (108 on at launch, 43 off until switched on), 15 partly, 49 have data and screens only, and 5 are not built.
- Documents: study 3.8, database design 3.14, requirements, traceability, business rules, behaviour models, the test plan and the readiness register 2.0.
- Since study 3.5 (schema files 1113 to 1129): know your customer for companies, logos and four-digit trip numbers, regular trips, booking modes and groups, seats chosen on each trip, charter with a deposit, separate departures and arrivals screens paired by a short code, Syria's administrative geography with field surveys, boundaries, corrected names and a map, and the photo settings screens.
- Since study 3.6 (schema file 1130): connections across carriers where no trip runs direct (Daraa to Aleppo through Damascus), with the risks accepted, flexible later trips, each carrier's policy for a missed trip and a booking changed to another trip.
- Since study 3.7 (schema files 1131 and 1132): the core of truck transport of goods and containers, inside Syria, to and from the port, in transit and across borders, with bills of lading, house bills and containers, consignments, the truck owner's prices, trucks and trailers, transport invoices per bill or container, and the consignment note and TCN the platform issues; and the money of a connection's missed trip held until the change window ends. The website was not changed, at the owner's request.

What remains before the pilot

- Owner inputs: approvals, the systems company, contracts (hosting, staging firm, penetration test, SMS and mail), legal texts and the pilot carriers.
- Evidence on staging and production for launch gates 1 to 8. Only staging or production evidence can pass a gate; the development team cannot.
- People: an on-call rota of three engineers, support and finance operations, each trained on its track.
- Data and acceptance: the pilot cities' stations and the carriers' fleets loaded, and the 45 acceptance scenarios signed.
- The apps in the stores, after the device matrix on real phones.

Planning assumptions

- The owner's inputs are in place by 13 November 2026. Every week of delay moves every later date by a week.
- If the go/no-go slips past late January 2027, the pilot moves to after Eid al-Fitr (about 22 March 2027), so that it does not start in Ramadan.
- Staging follows the gate closure plan: about three weeks once the servers, the on-call rota, the audit bucket and the penetration test firm exist.
- The pilot is paid in cash and uses the platform's own sign-in. Card payments, identity providers and the tax authority link follow their contracts and specifications; they do not hold the pilot.
- Later phases: their tables, interfaces and many screens are built and switched off. Each window covers the workflows that are still data only, the phase's acceptance gate and any field trial. One continuing team; phases that depend on authorities or contracts are indicative.
- Ramadan and Eid dates are approximate because they follow the lunar calendar.

What changed since version 1.0

- Version 1.0 planned twelve months of programming for Phase 1, with the pilot on 4 October 2027. The software of Phase 1 is now built, so the pilot moves to 4 January 2027, and Phase 1 closes on 9 April 2027 instead of 26 November 2027.
- The critical path is no longer programming. It is the owner's inputs, the staging evidence, the people and the acceptance tests.
- A lane for the owner, contracts and authorities is added. Dashed bars depend on an outside party.
- Boarding stations, counter sales and the departure board moved from Phase 7 into the first release (owner's decision, October 2026).
- The later phases start about seven months earlier, and the roadmap ends in 2031 instead of 2032.

Sources: Analysis and Design Study 3.8 (sections 21, 22, 22.6 to 22.9), the gate closure plan (docs/operations/GATE_CLOSURE_PLAN.md), the release map, the use case document 2.1 and the repository at schema file 1132, 18 October 2026. Version 3.2.
